



RAJ GARG & ASSOCIATES

CHARTERED ACCOUNTANTS

TO WHOMSOEVER IT MAY CONCERN

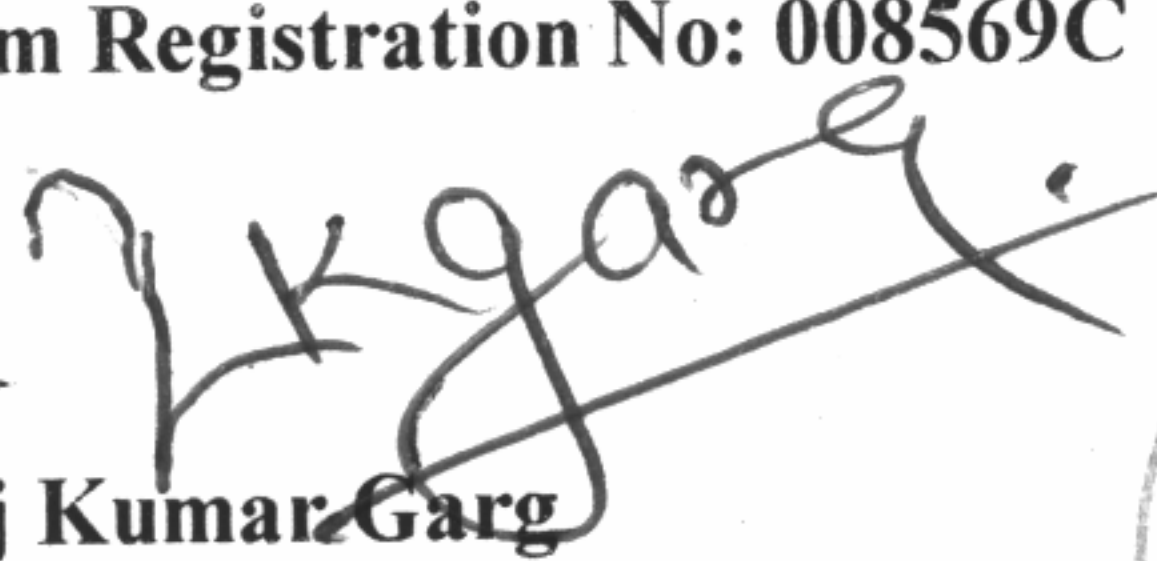
On the basis of information/documents, unaudited books of accounts and other records produced before us by M/s. Ajay Enterprises Pvt. Ltd. having regd. office at 8th Floor, Eros Corporate Tower, Nehru Place, New Delhi-110019, this is to certify that the estimated cost of the project, total cumulative cost incurred on construction of the project as on 31 Dec,2022 and 31 Mar,2023 and percentage of remaining work in term of cost for "Edenwood Towers", Village-Lakkarpur, Sector 39, Faridabad, Haryana (Regn. No. HRERA-PKL-FBD-92-2019 dated 24.01.2019) are as under:

(Amount in Rs Lakhs)

Sr. No.	Particulars	Estimated Cost*	Cost Incurred			Percentage of Remaining Work as at		
			up to 31 Dec , 2022	up to 31 Mar, 2023	For the quarter ended 31 Mar,2023	Balance cost to be incurred as on 31 Mar, 2023	31 Dec ,2022	31 Mar ,2023
1	Cost of Land	1.79	1.79	1.79	-	-	0.00%	0.00%
2	Cost of Construction of Apartments	9,671.92	5,864.79	6,161.31	296.52	3,510.61	39.36%	36.30%
3	Cost of Infrastructure & Other Structure	548.04	-	-	-	548.04	100.00%	100.00%
4	Other costs incl. EDC, Taxes, Levies & Overheads	2,559.84	2,121.09	2,213.14	92.05	346.70	17.14%	13.54%
Total		12,781.59	7,987.67	8,376.24	388.57	4,405.35	37.51%	34.47%

*The estimated cost has been taken on the basis of budget prepared by the management of the Company.

For RAJ GARG & ASSOCIATES
Chartered Accountants
Firm Registration No: 008569C


Raj Kumar Garg
Partner
Membership No.
UDIN:-23091706BGXNIB1467



Place: New Delhi
Date : 14.04.2023
