



GLOBAL HEIGHTS



CBRE

CONTENTS

1.	Safety precautions to be followed.
2.	Site photographic report.
3.	Quality photographic report - Before and after rectification.
4.	Work progress report

Safety precautions to be followed

PROTECT YOURSELF

PERSONAL PROTECTION EQUIPMENT IS IMPORTANT TO YOU!

HEAD

HARD HATS PROTECT AGAINST FALLING OBJECTS OR HEAD BUMPS. THEY RESIST PENETRATION AND ABSORB SHOCK.

ADJUST HEAD BAND TO ALLOW FOR SUFFICIENT CLEARANCE BETWEEN THE SHELL AND THE HEADBAND. INSPECT SHELL AND ALL COMPONENTS FOR SLIGHTS OF DAMAGE.



RESPIRATORY

RESPIRATORS PROTECT AGAINST CONTAMINATED AIR, SELECTED ON THE BASIS OF THE HAZARD. WORKERS SHOULD BE FIT-TESTED TO INSURE A TIGHT SEAL.

INSPECT BEFORE AND AFTER EACH USE OR MONTHLY, IF NOT USED ROUTINELY. CLEAN AND STORE TO PROTECT AGAINST DAMAGE.



EYES & FACE

SAFETY GLASSES, GOGGLES AND FACE SHIELDS PROTECT EYES OR FACE FROM FLYING PARTICLES, MOLTEN METAL, LIQUID CHEMICALS, ACID OR CAUSTIC LIQUIDS, CHEMICAL GASES, VAPORS & RADIATION.

FITTING AND SELECTION OF GLASSES SHOULD BE PERFORMED BY SKILLED PERSONNEL. INSPECT AND CLEAN LENSES; VISUALLY INSPECT FRAMES.



HEARING

HEARING PROTECTION PREVENTS PERMANENT IRREVERSIBLE HEARING DAMAGE.

SAFETY MANAGERS SELECT THE BEST TYPE FROM A CHOICE OF DISPOSABLE, PREFORMED EARPLUGS OR EARMUFFS. MUST BE PROPERLY FITTED IF PROTECTION LEVELS ARE TO BE ATTAINED. WASH HANDS BEFORE INSERTING PLUGS. NON-DISPOSABLE PLUGS MUST BE CLEANED.



HANDS

GLOVES PROTECT HANDS FROM CUTS AND ABRASIONS, HARMFUL TEMPERATURE EXTREMES, OR CHEMICAL INJURY.

AFTER ANALYZING JOB ACTIVITY WITH RESPECT TO DEXTERITY NEEDED AND DEGREE OF EXPOSURE TO HAZARD, SAFETY MANAGER SELECTS THE APPROPRIATE GLOVE. INSPECT PRIOR TO WEARING; REPLACE AS NECESSARY.



FEET

SAFETY SHOES PROTECT AGAINST INJURY FROM FALLING OR ROLLING OBJECTS, MOLTEN METAL, HOT SURFACES AND WET SLIPPERY SURFACES.

MUST BE STURDY WITH IMPACT RESISTANT TOES. SOME OFFER METAL INSOLES AND METATARSAL GUARDS. SELECT THE APPROPRIATE SHOE.




A Workplace Injury Occurs Every 18 Seconds

© 2004 PINKSTON ELECTRONICS
Developed in partnership with Safety Manager
for Corporate Safety Public



GLOBALHEIGHTS
www.affordablehomessohna.in

PROGRESS PHOTOGRAPHS

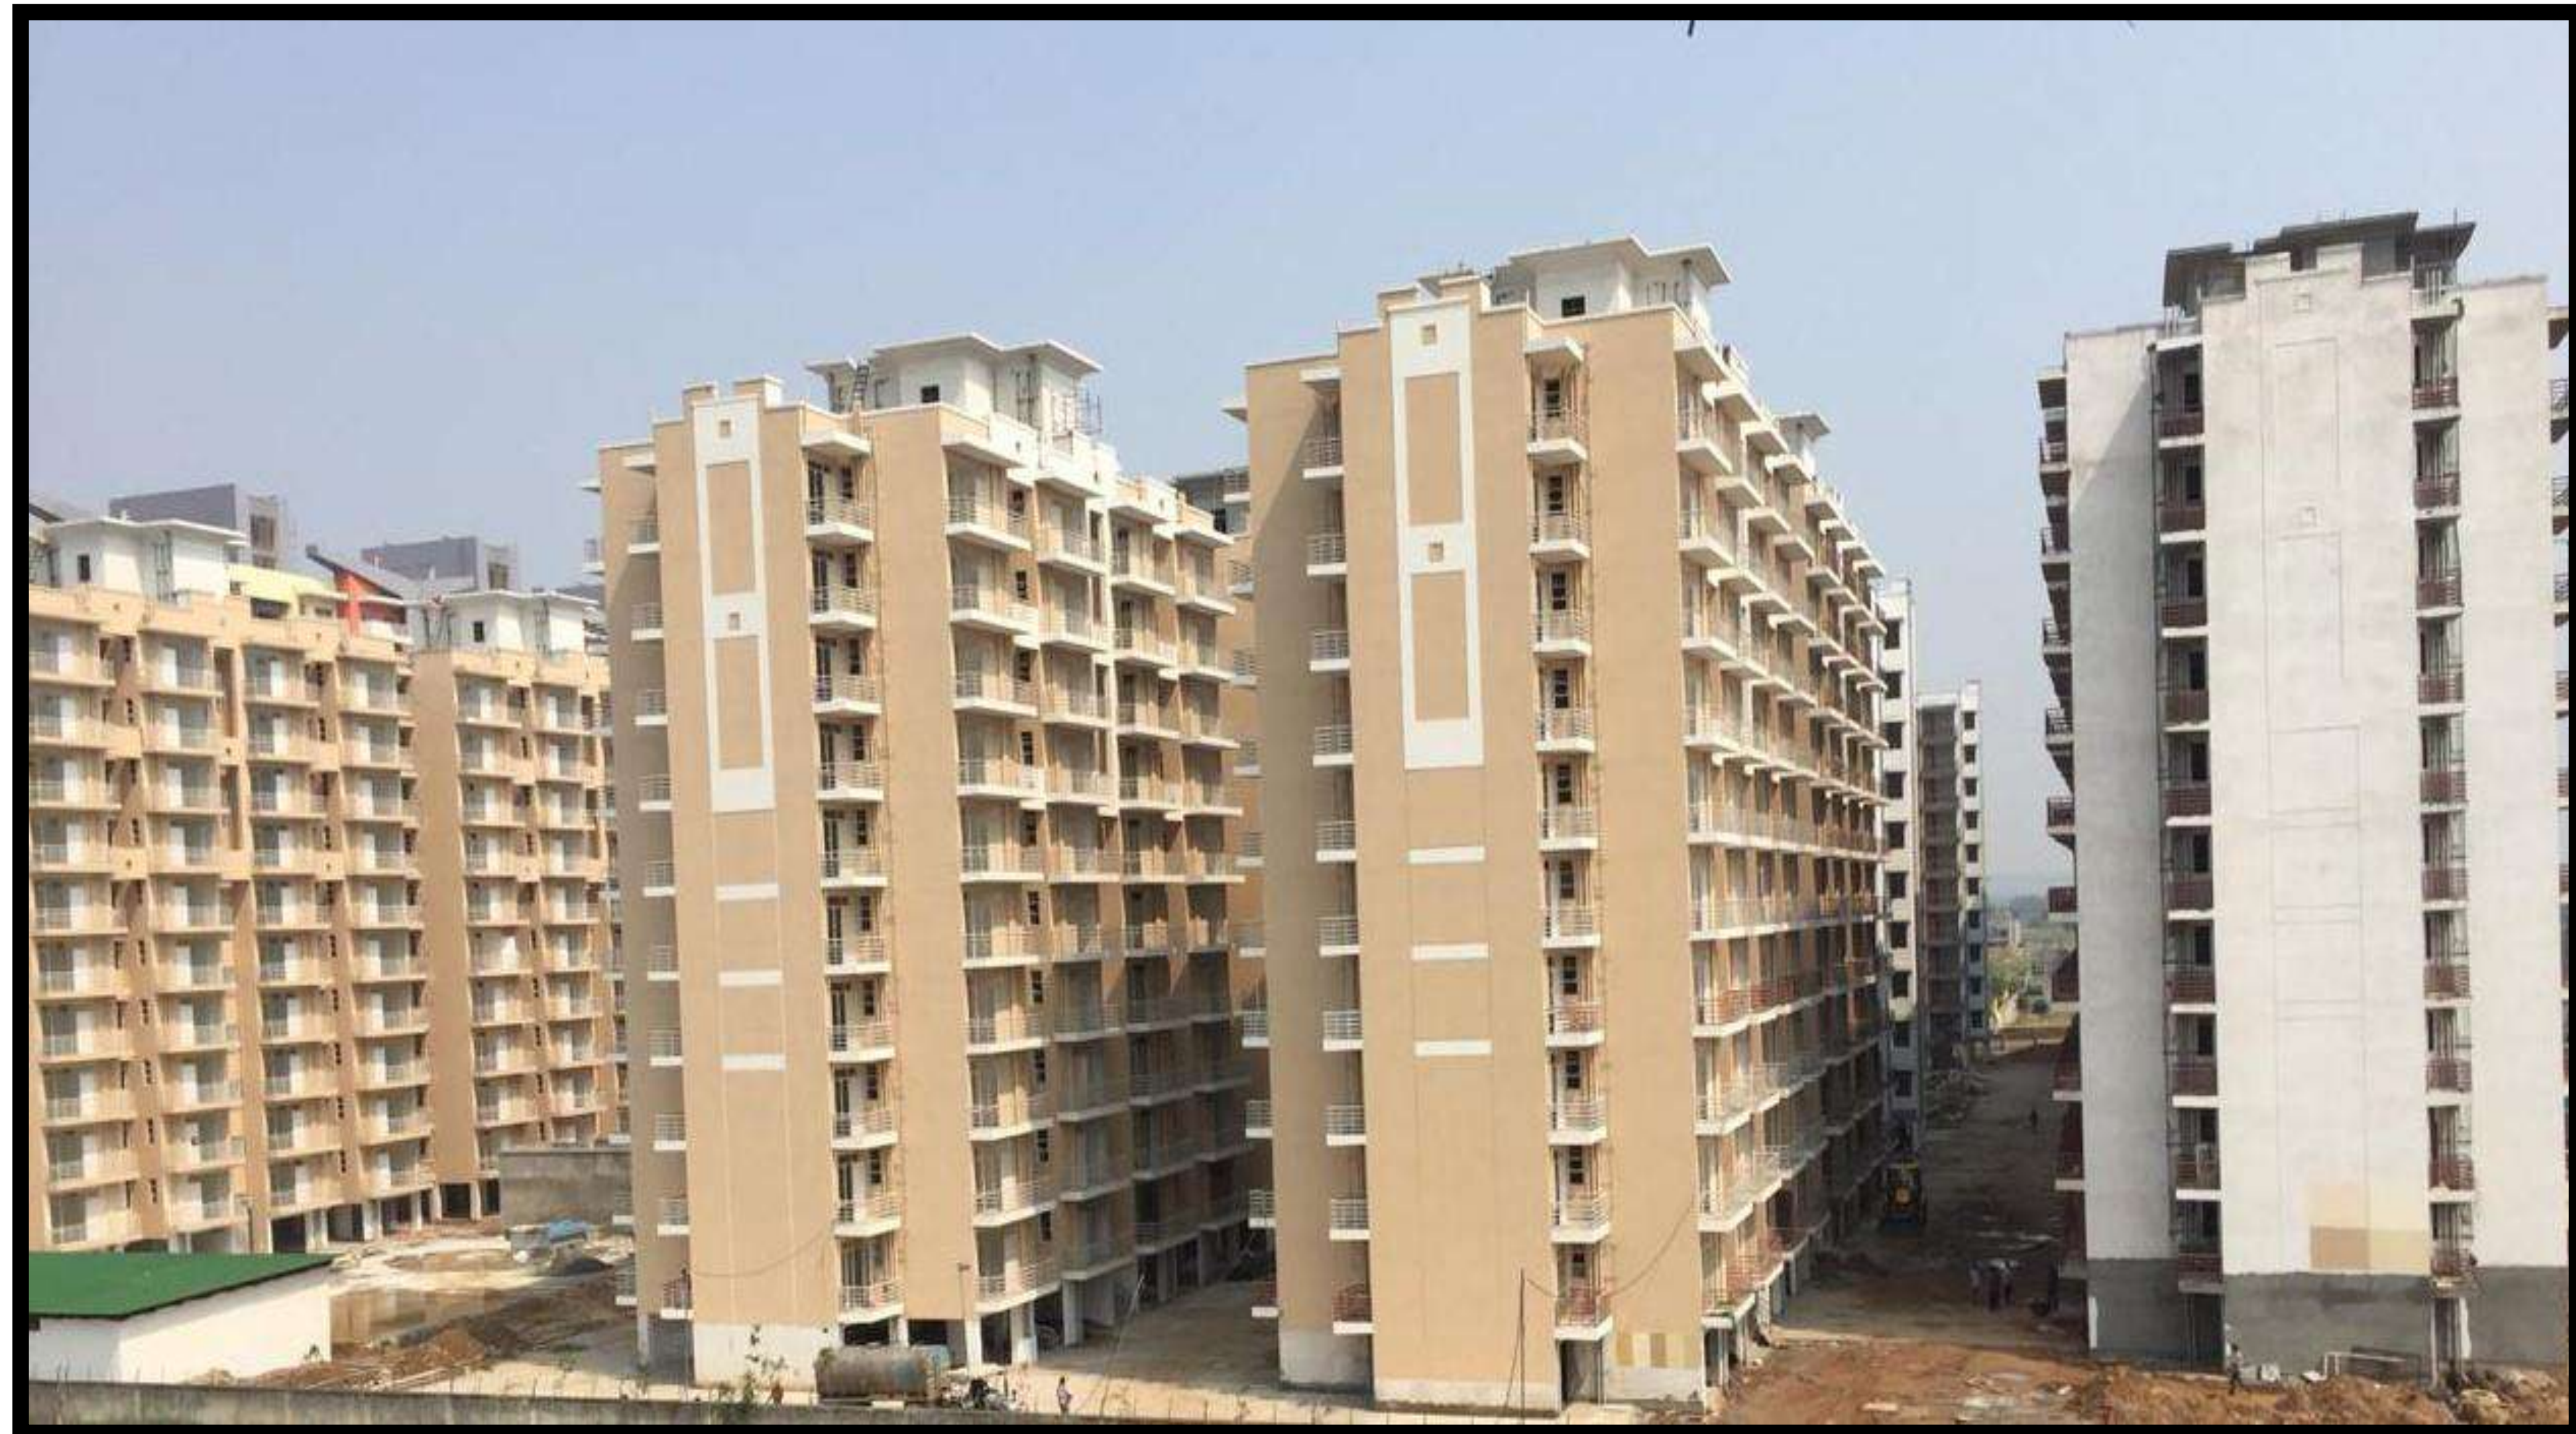

GLOBALHEIGHTS
www.affordablehomesohna.in

Breez Builders & Developers (P) LTD.

CBRE

PROGRESS PHOTOGRAPHS



Glass Work is in Progress

PROGRESS PHOTOGRAPHS



PROGRESS PHOTOGRAPHS



Putty Work is in Progress

PROGRESS PHOTOGRAPHS




UGT Water Proofing Work is in Progress

PROGRESS PHOTOGRAPHS



Road Work – Back side of Tower- 18

PROGRESS PHOTOGRAPHS

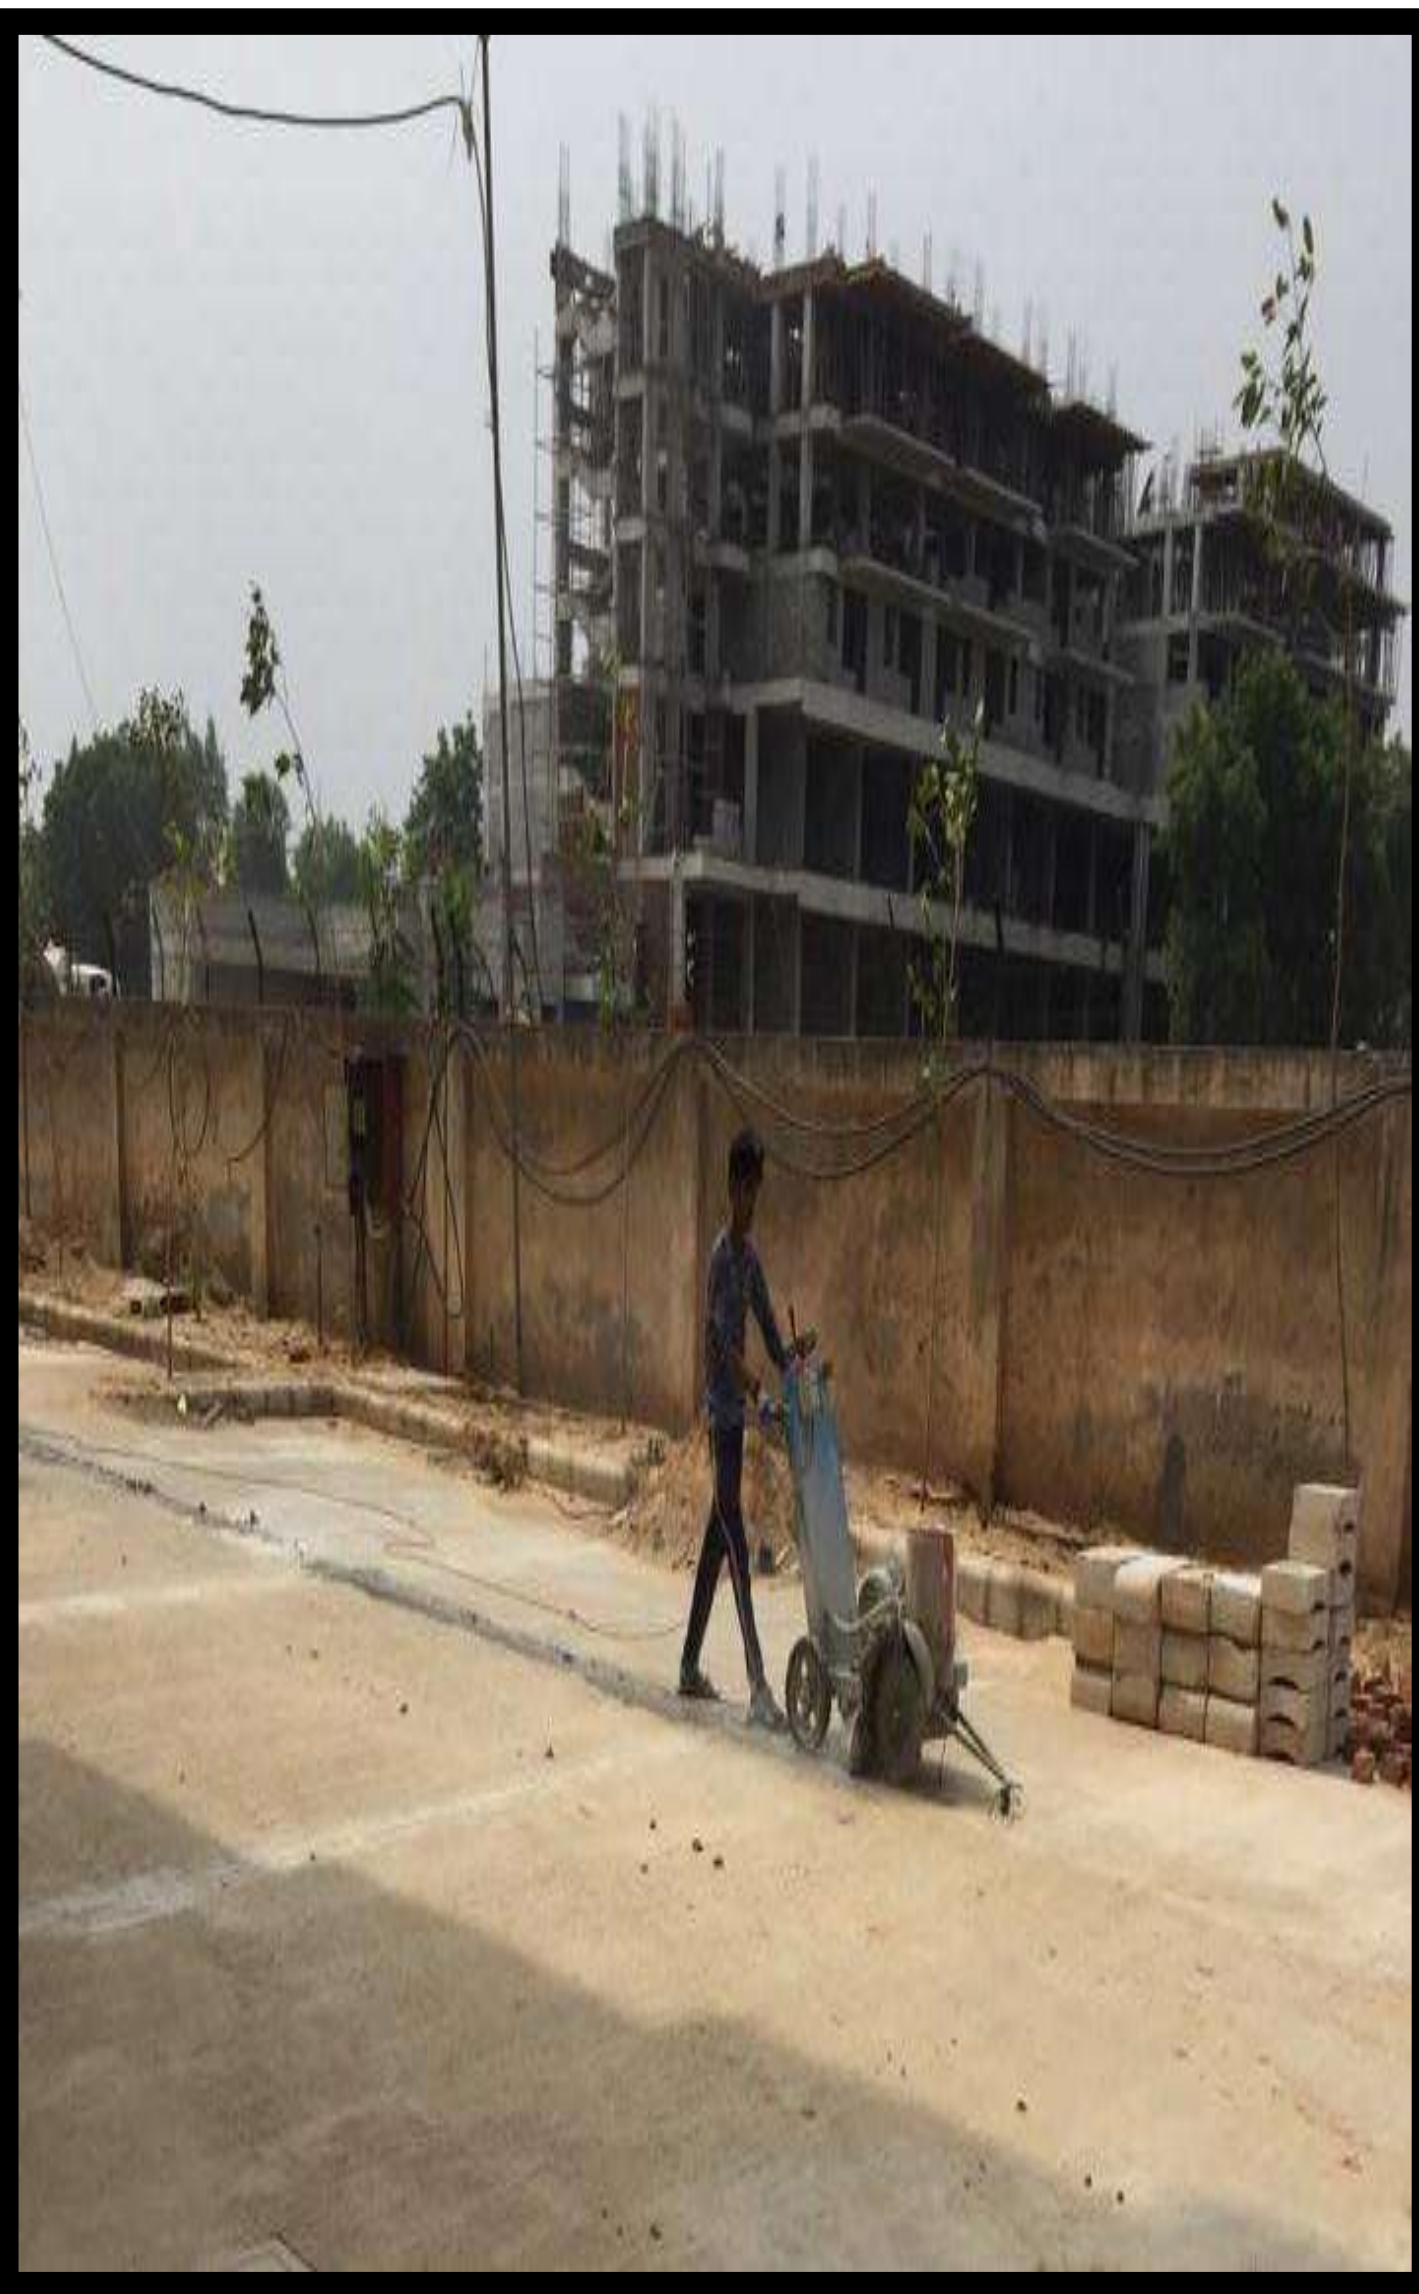

Groove Cutting Work is in progress

PROGRESS PHOTOGRAPHS



Sub Main Meter Board Termination Work is in progress




GLOBALHEIGHTS
www.affordablehomesohna.in

Breez Builders & Developers (P) LTD.

CBRE

PROGRESS PHOTOGRAPHS

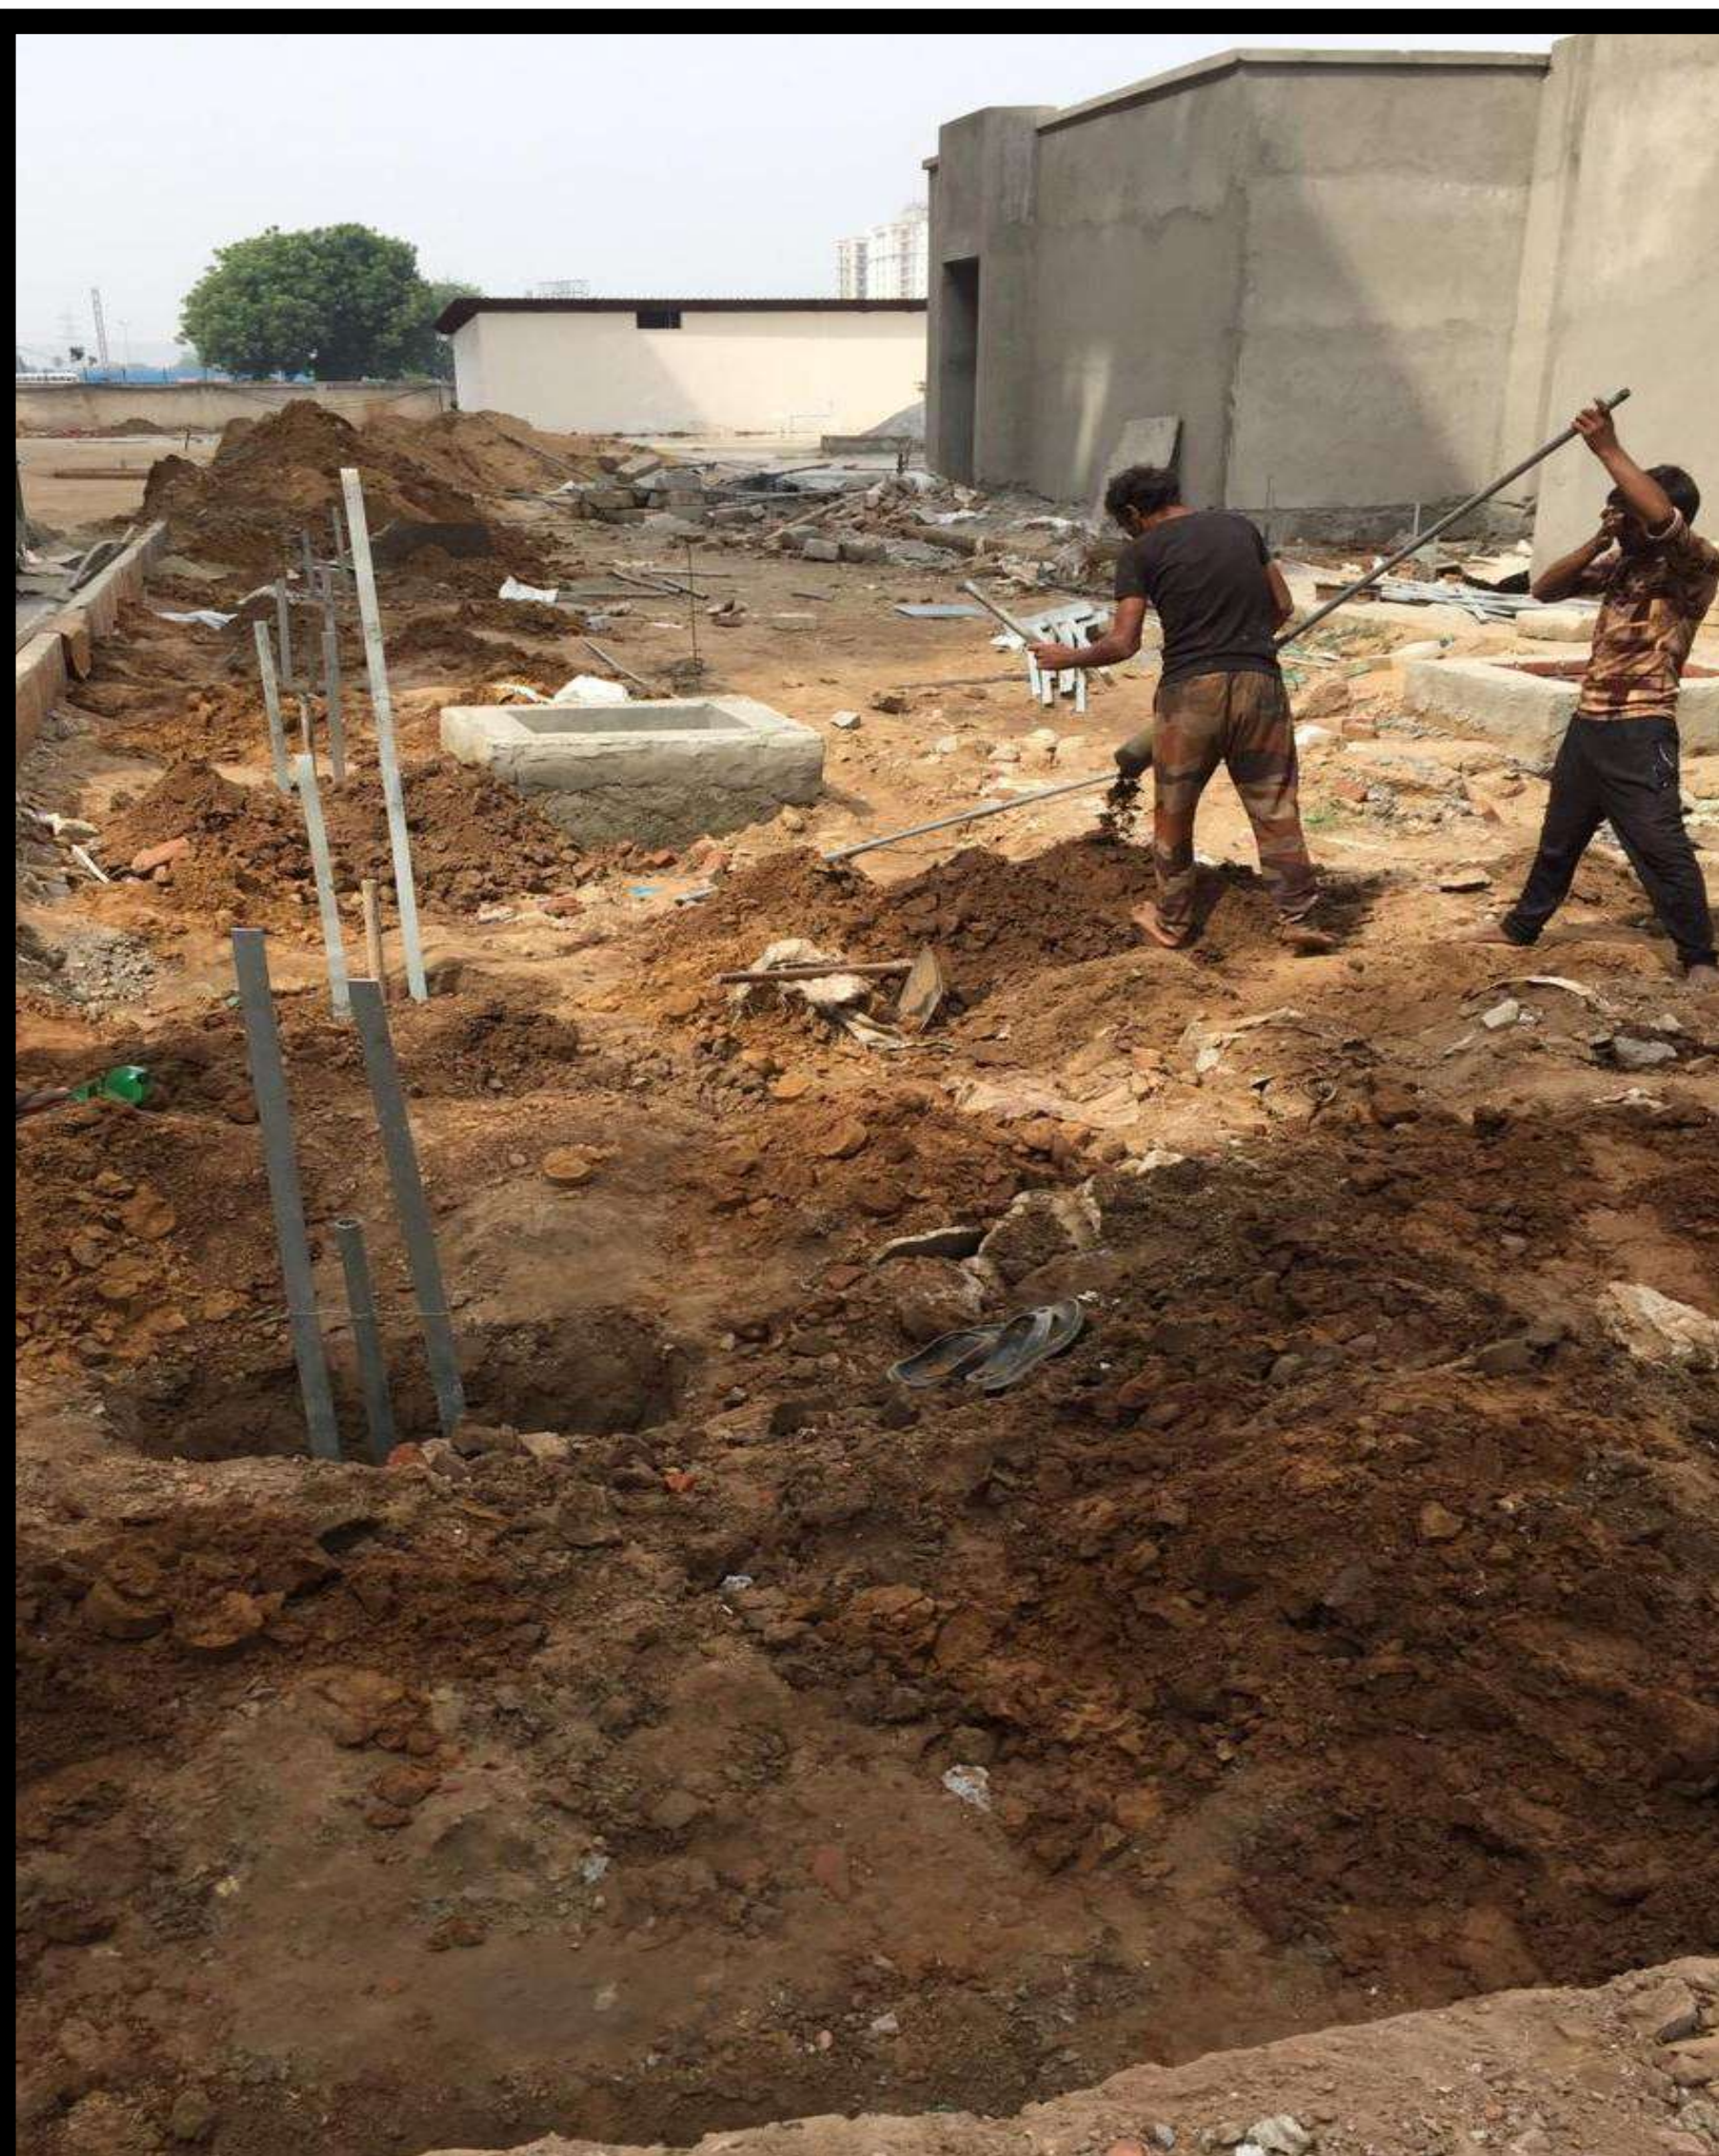



Earthing Pit work is in progress

PROGRESS PHOTOGRAPHS



FTTH Room Plaster work

PROGRESS PHOTOGRAPHS

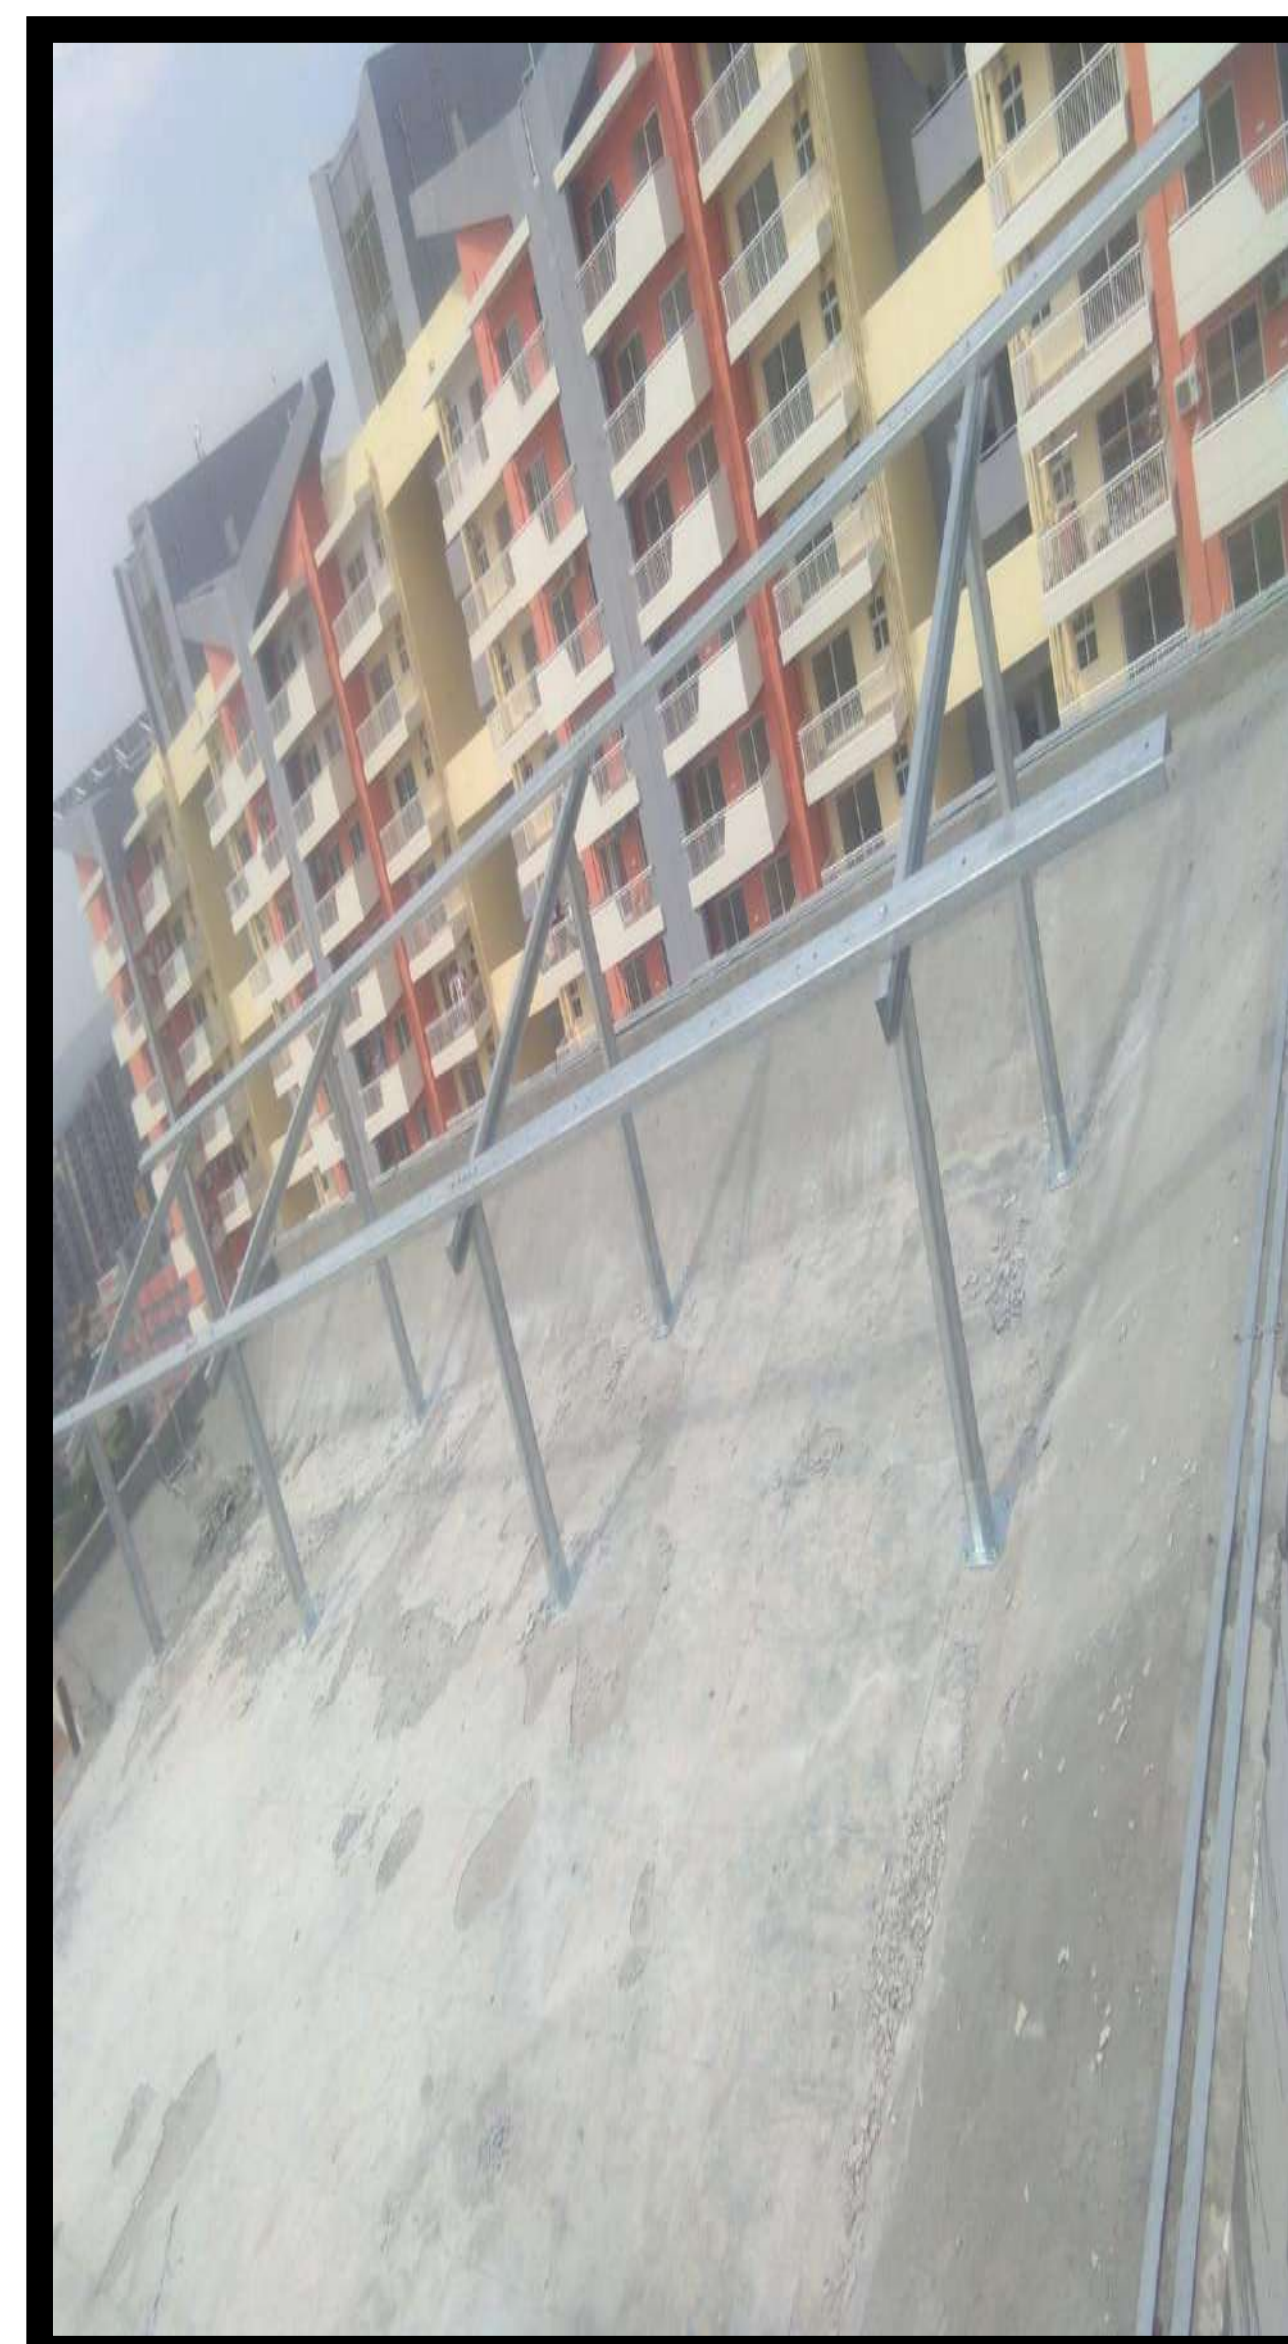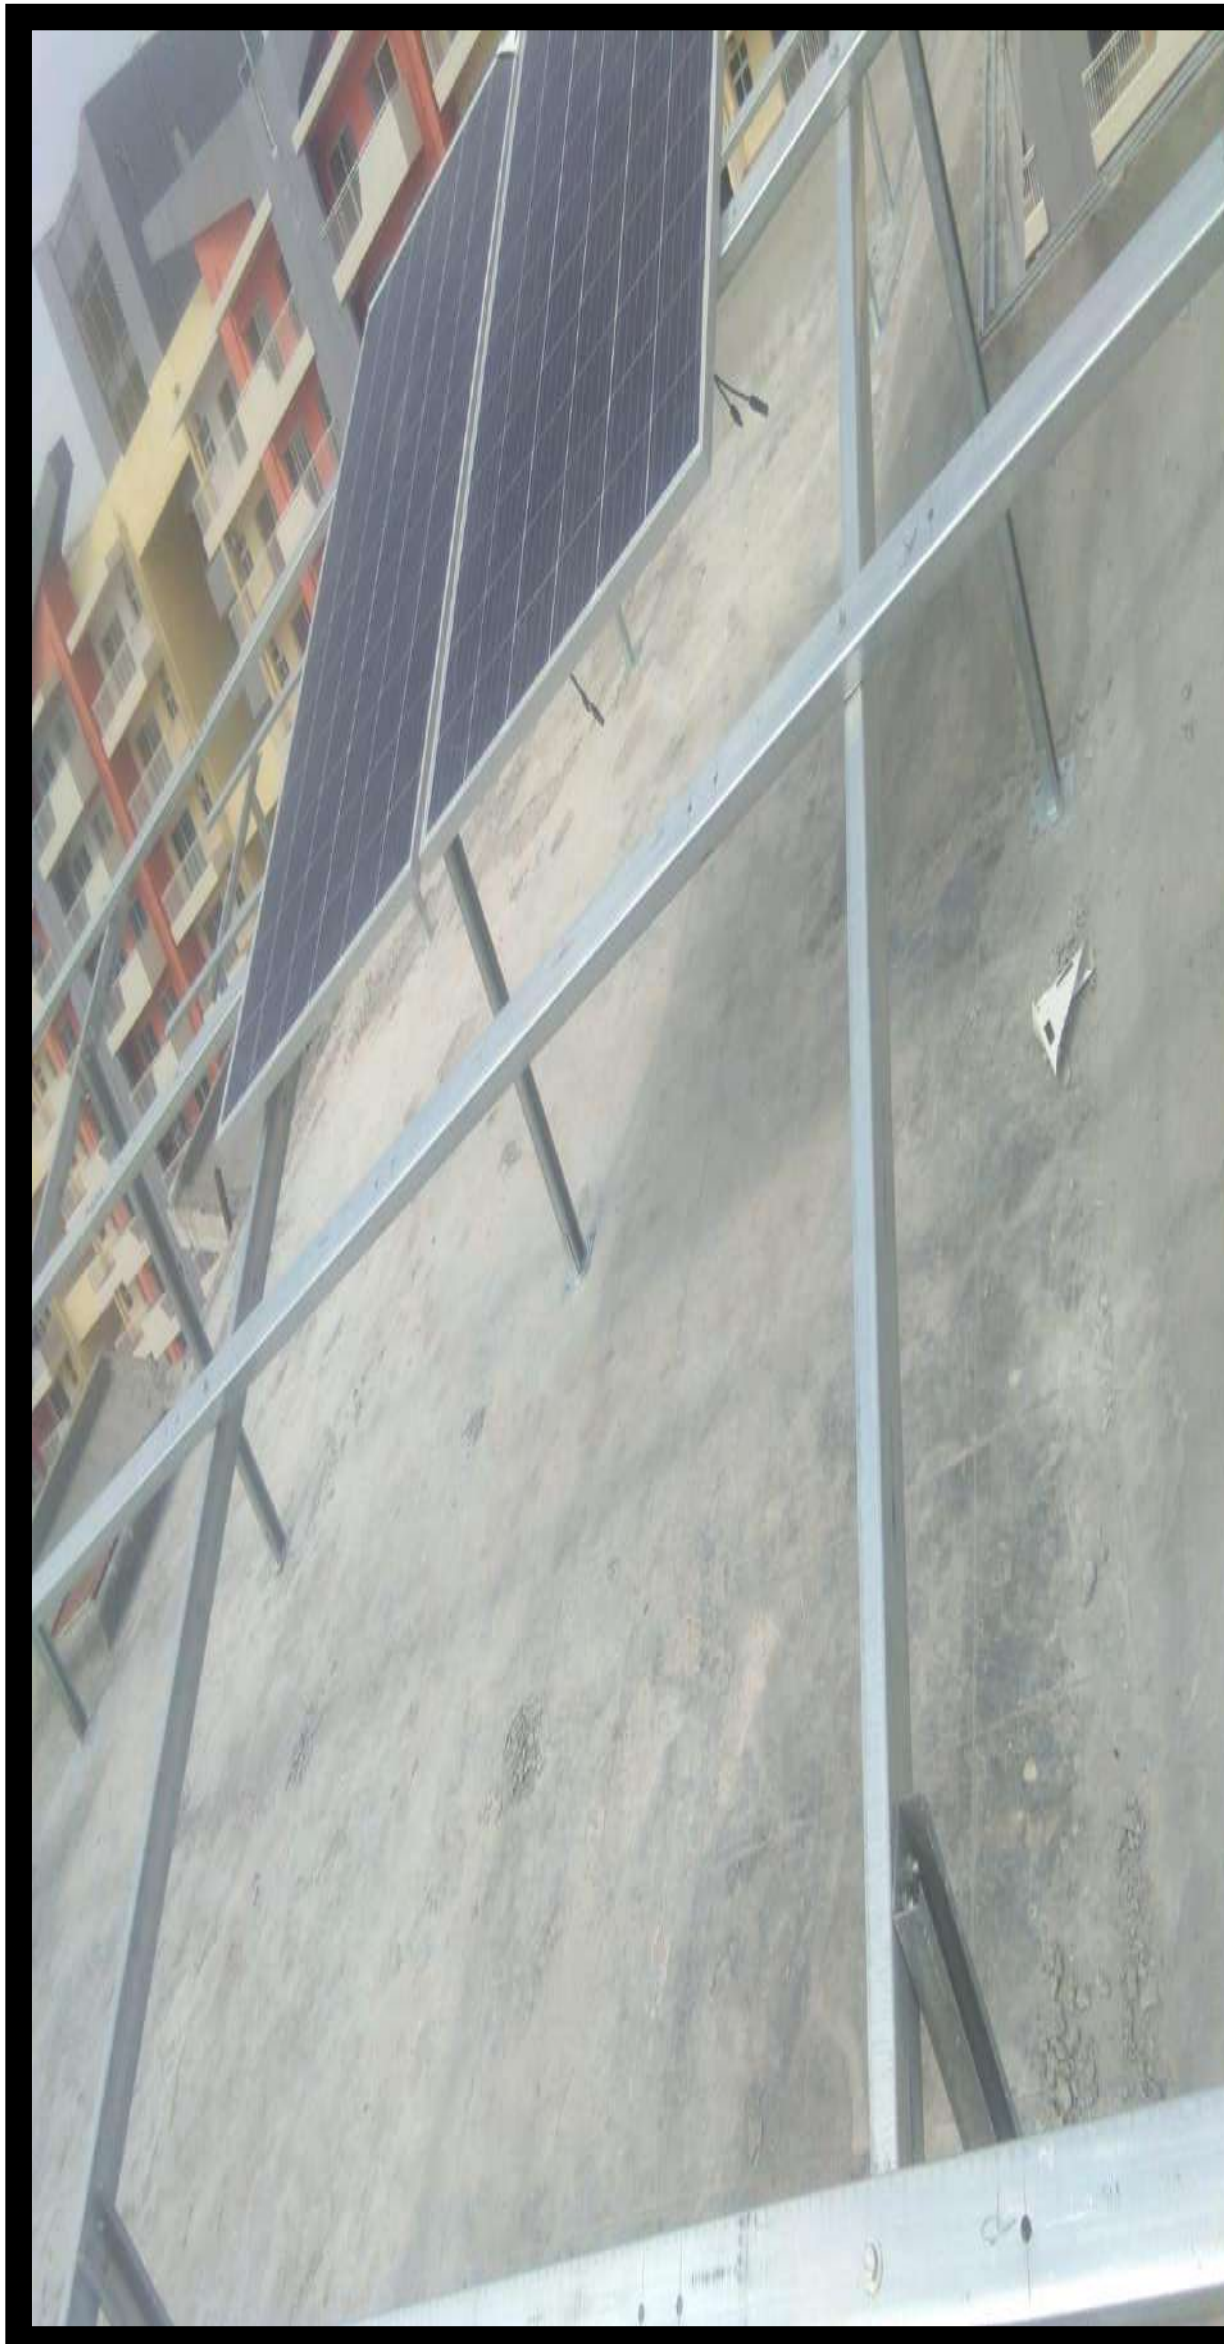

Solar Panel Framing Work – Tower – 15 & 16

PROGRESS PHOTOGRAPHS





Guard Room



STP Entrance Plaster work

PROGRESS PHOTOGRAPHS

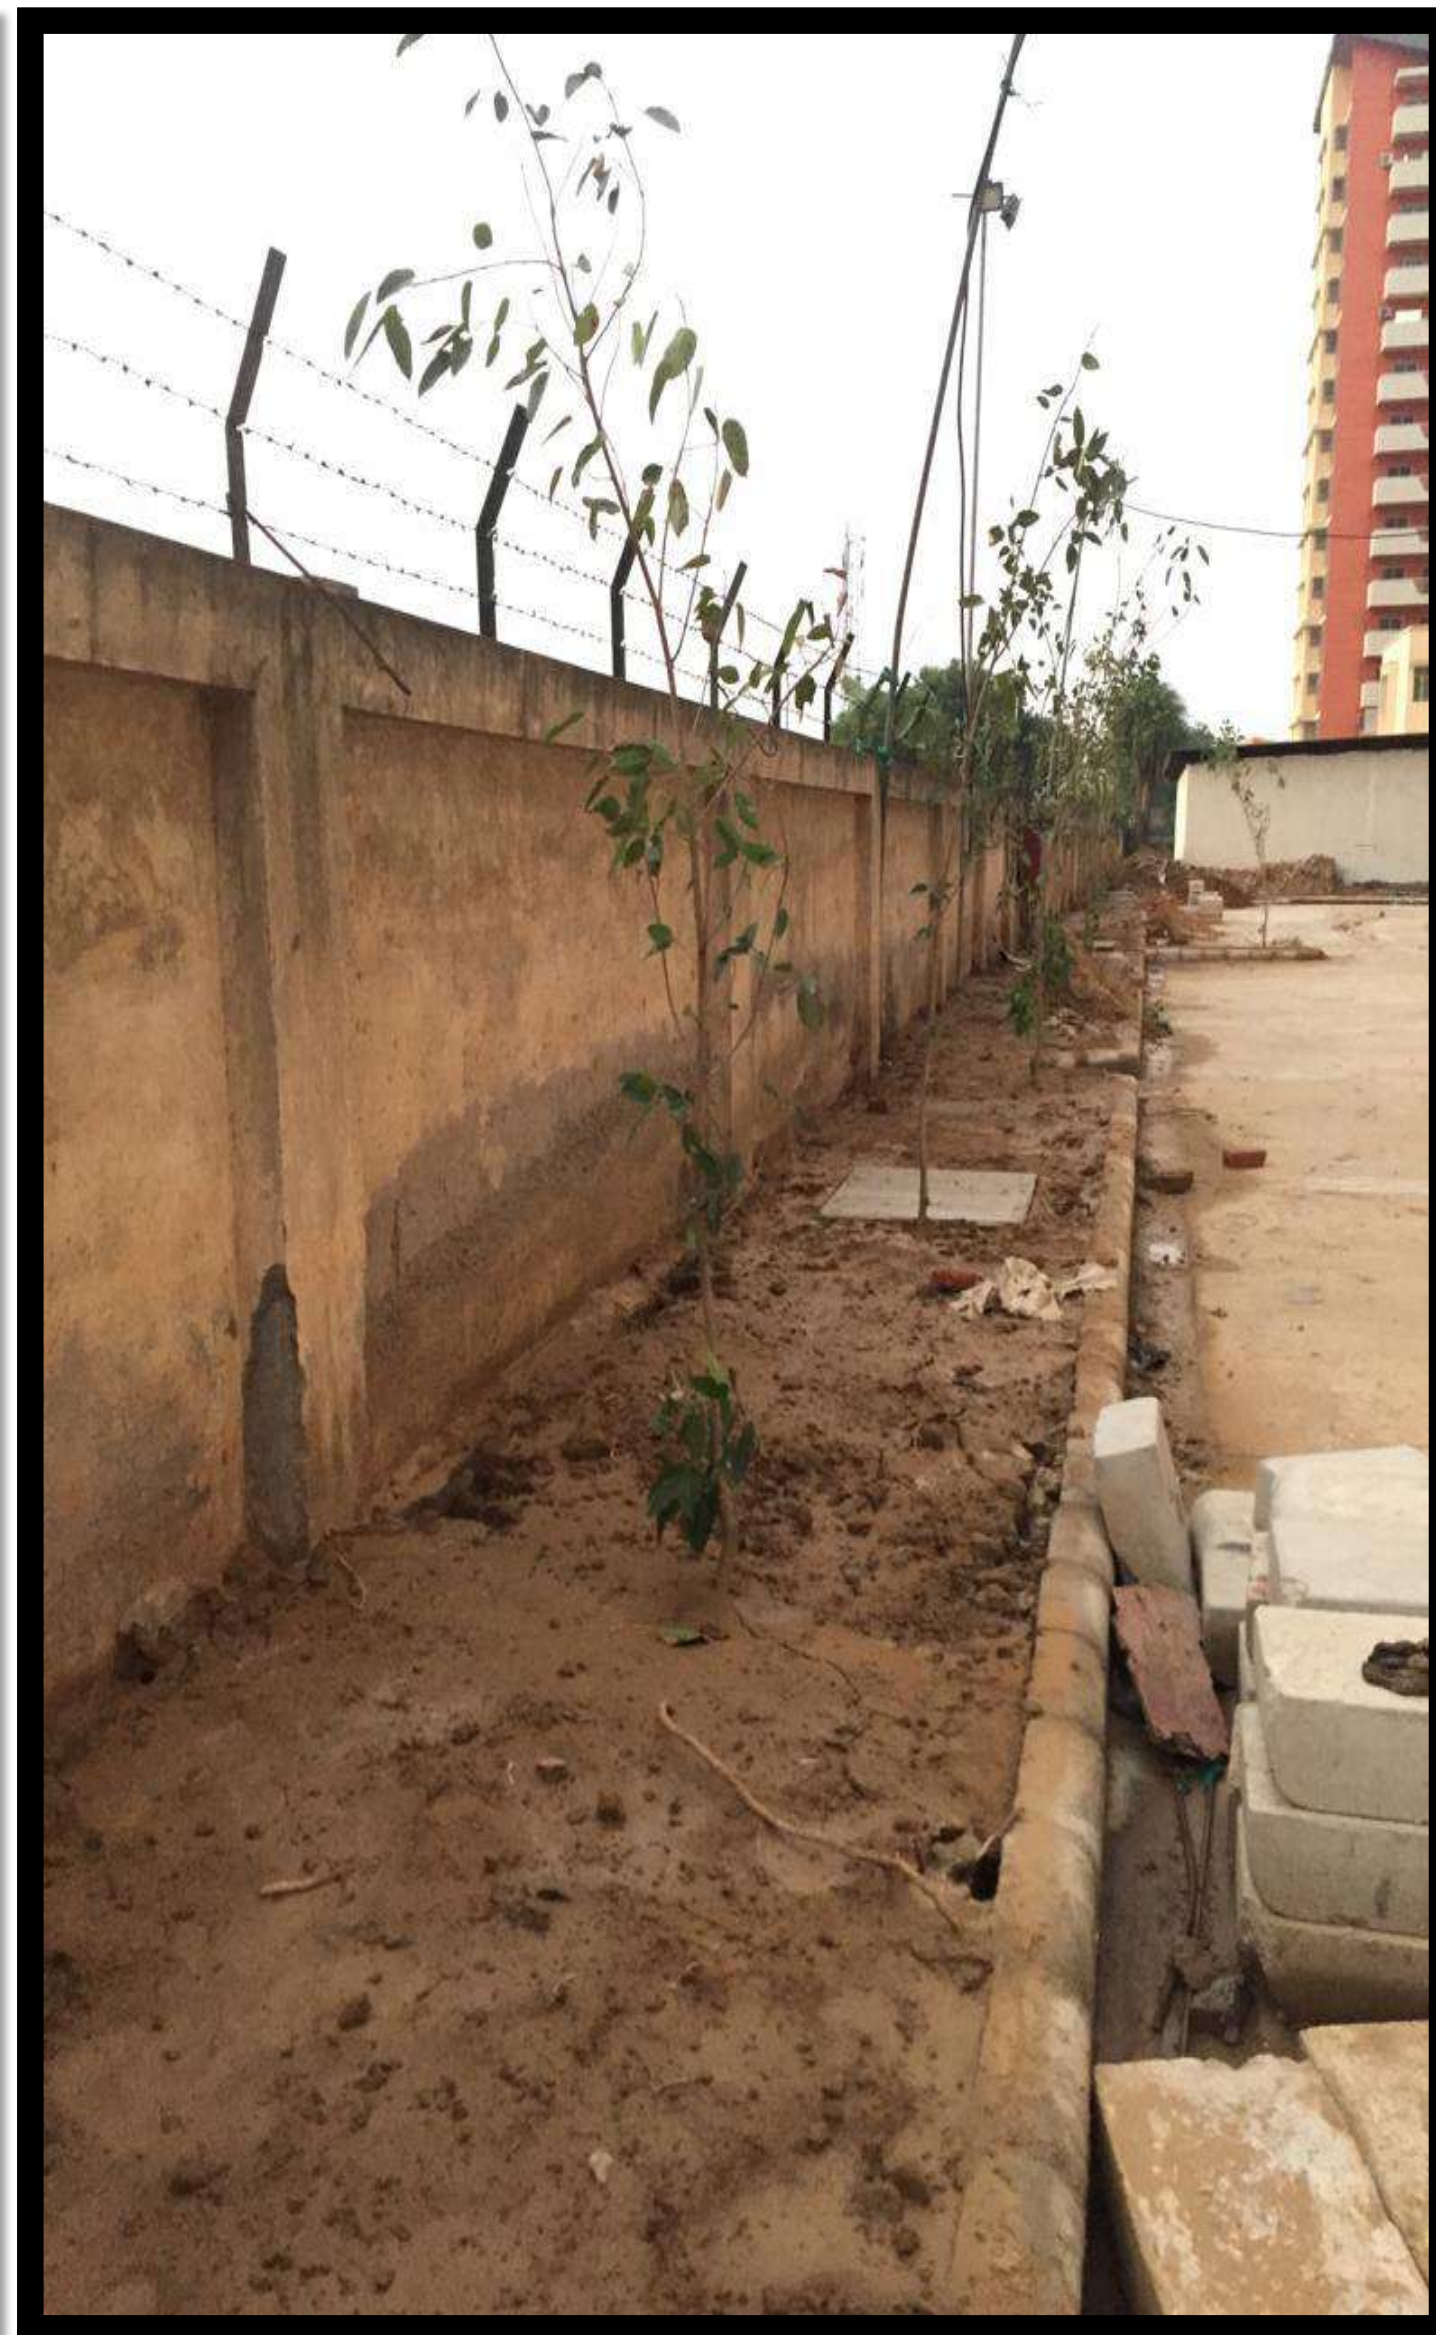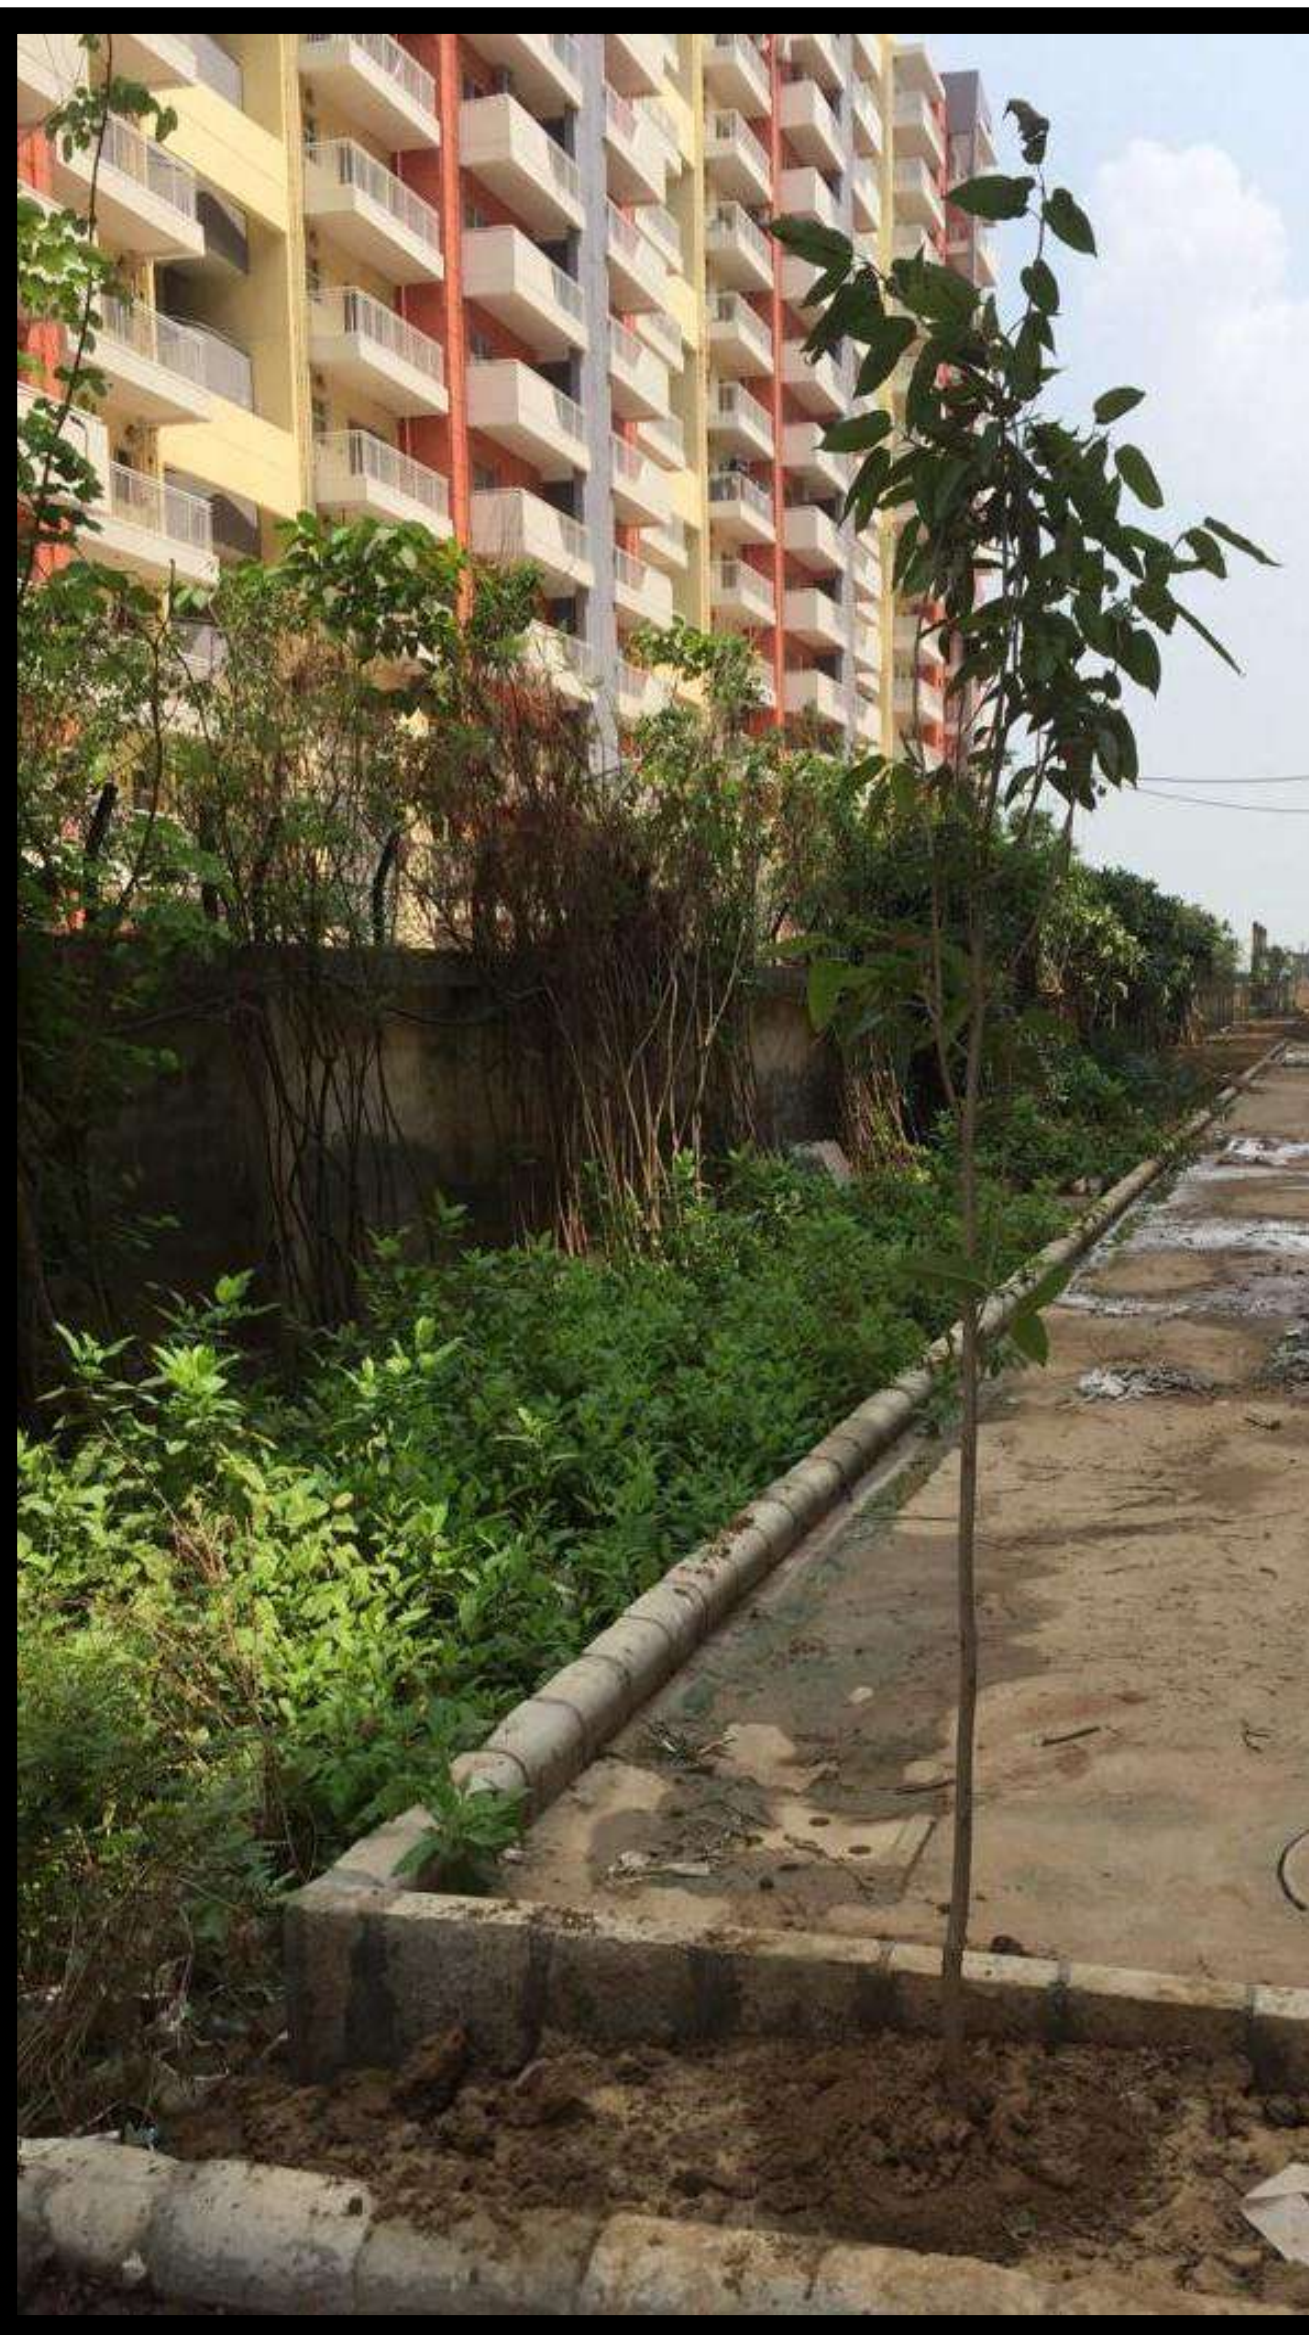

Horticulture Work

ROAD WORK PROGRESS MARKING DRAWING



Road Work

PROGRESS PHOTOGRAPHS



Project: /	Global Heights								
Document Number:	CBRE-Global Heights- Snag list.								
Document Title:	Snag List								
Date:	Till 7.10.2019								

CBRE

S.No	Site	Area / Location	Issues / Defects / Non-conformance	Photographic issue	Comment Date	Critical/ Non Critical	Responsibility	Status (Open / Closed)	Photographic issue	Remarks
1.	Global Height's	T-10	Finishing not properly done.		7-10-2019	Critical	Site team	Open		
2.	Global Height's	T-14	OHT Seepage / Leakage.		7-10-2019	Critical	Site team	Open		
3.	Global Height's	T-4	Plaster repairing pending		12-08-2019	Critical	Site team	Open		
4.	Global Height's	T-10	Crack on external side wall of tower in max. towers		26-08-2019	Critical	Site team	Open		



GLOBALHEIGHTS
www.affordablehomessohna.in

Breez Builders & Developers (P) LTD.

CBRE

Project:			Global Heights								CBRE
Document Number:			CBRE-Global Heights- Snag list.								
Document Title:			Snag List								
Date:			Till 07.10.2019								
S.No	Site	Area / Location	Issues / Defects / Non-conformance	Photographic issue	Comment Date	Critical/ Non Critical	Responsibility	Status (Open / Closed)	Photographic issue	Remarks	
5.	Global Height's	T-10	Plaster repairing pending.		07-10-2019	Critical	Site team	Open			
6.	Global Height's	T-10	Trimix road grooves not in alignment.		07-10-2019	Critical	Site team	Open			
7.	Global Height's	T-17	Finishing pending.		07-10-2019	Critical	Site team	Open			
8.	Global Height's	T-12	Stilt Floor Ceiling Repair		07-10-2019	Critical	Site team	Open			

Project:	Global Heights								
Document Number:	CBRE-Global Heights- Snag list.								
Document Title:	Snag List								
Date:	Till 07.10.2019								

CBRE

S.No	Site	Area / Location	Issues / Defects / Non-conformance	Photographic issue	Comment Date	Critical/ Non Critical	Responsibility	Status (Open / Closed)	Photographic issue	Remarks
9.	Global Height's	T-10	Not properly finished by regmark & putty.		12-08-2019	Critical	Site team	Open		
10.	Global Height's	T-5 in max. flats	Plaster repairing pending in max. towers.		18-07-2019	Critical	Site team	Open		
11.	Global Height's	T- 12	Bore packing not done on stilt floor.		07-10-2019	Critical	Site team	Open		
12.	Global Height's	In Max. Towers.	Cracks in brick koba.		07-10-2019	Critical	Site team	Open		



GLOBALHEIGHTS
www.affordablehomessohna.in

Breez Builders & Developers (P) LTD.

CBRE

Project:	Global Heights								
Document Number:	CBRE-Global Heights- Snag list.								
Document Title:	Snag List								
Date:	Till 07.10.2019								

CBRE

S.No	Site	Area / Location	Issues / Defects / Non-conformance	Photographic issue	Comment Date	Critical/ Non Critical	Responsibility	Status (Open / Closed)	Photographic issue	Remarks
13.	Global Height's	T-12	Kerb stone & saucer drain is broken near side of tower 12.		26-08-2019	Critical	Site team	Open		
14.	Global Height's	Near T-20	Pointing is not done in kerb stone.		07-10-2019	Critical	Site team	Open		
15.	Global Height's	T- 4	Balcony edges not properly finished in Maximum Tower.		23-08-2019	Critical	Site team	Open		




GLOBALHEIGHTS
www.affordablehomessohna.in

Breez Builders & Developers (P) LTD.

CBRE


SUMMERIZED TOWER WISE WORK STATUS

Tower 1 To 5 Work Status

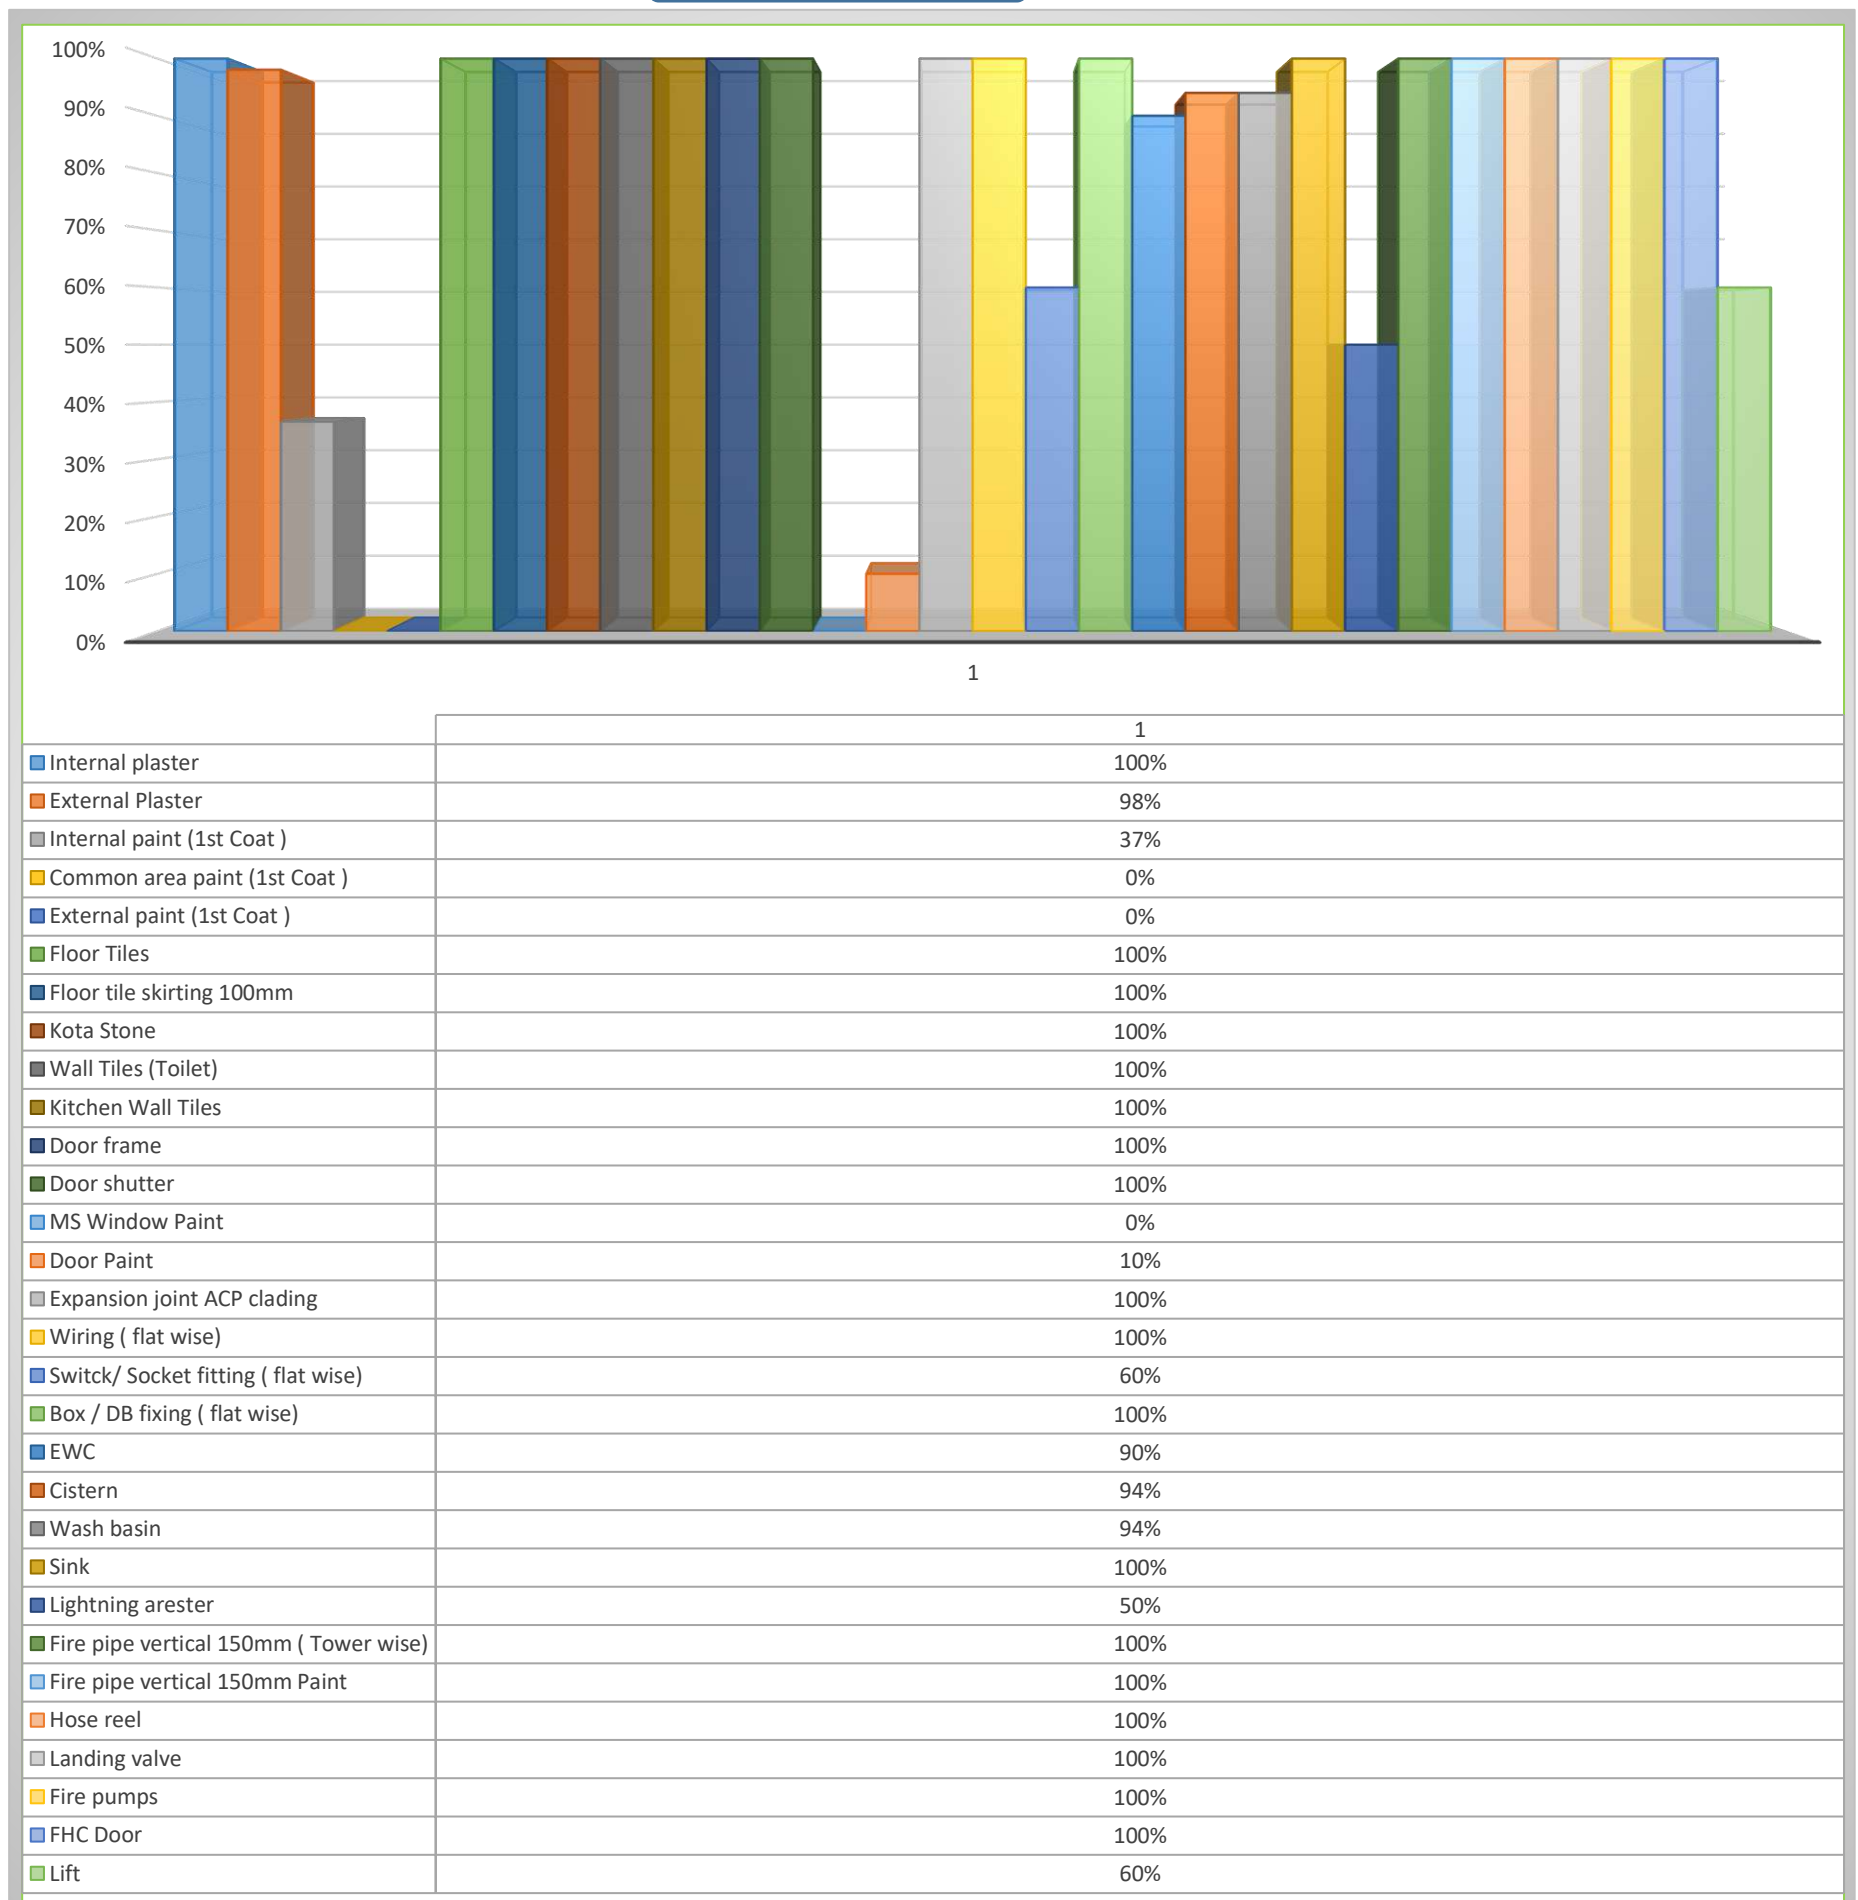


SUMMERIZED TOWER WISE WORK STATUS

Tower 6 To 17 Work Status

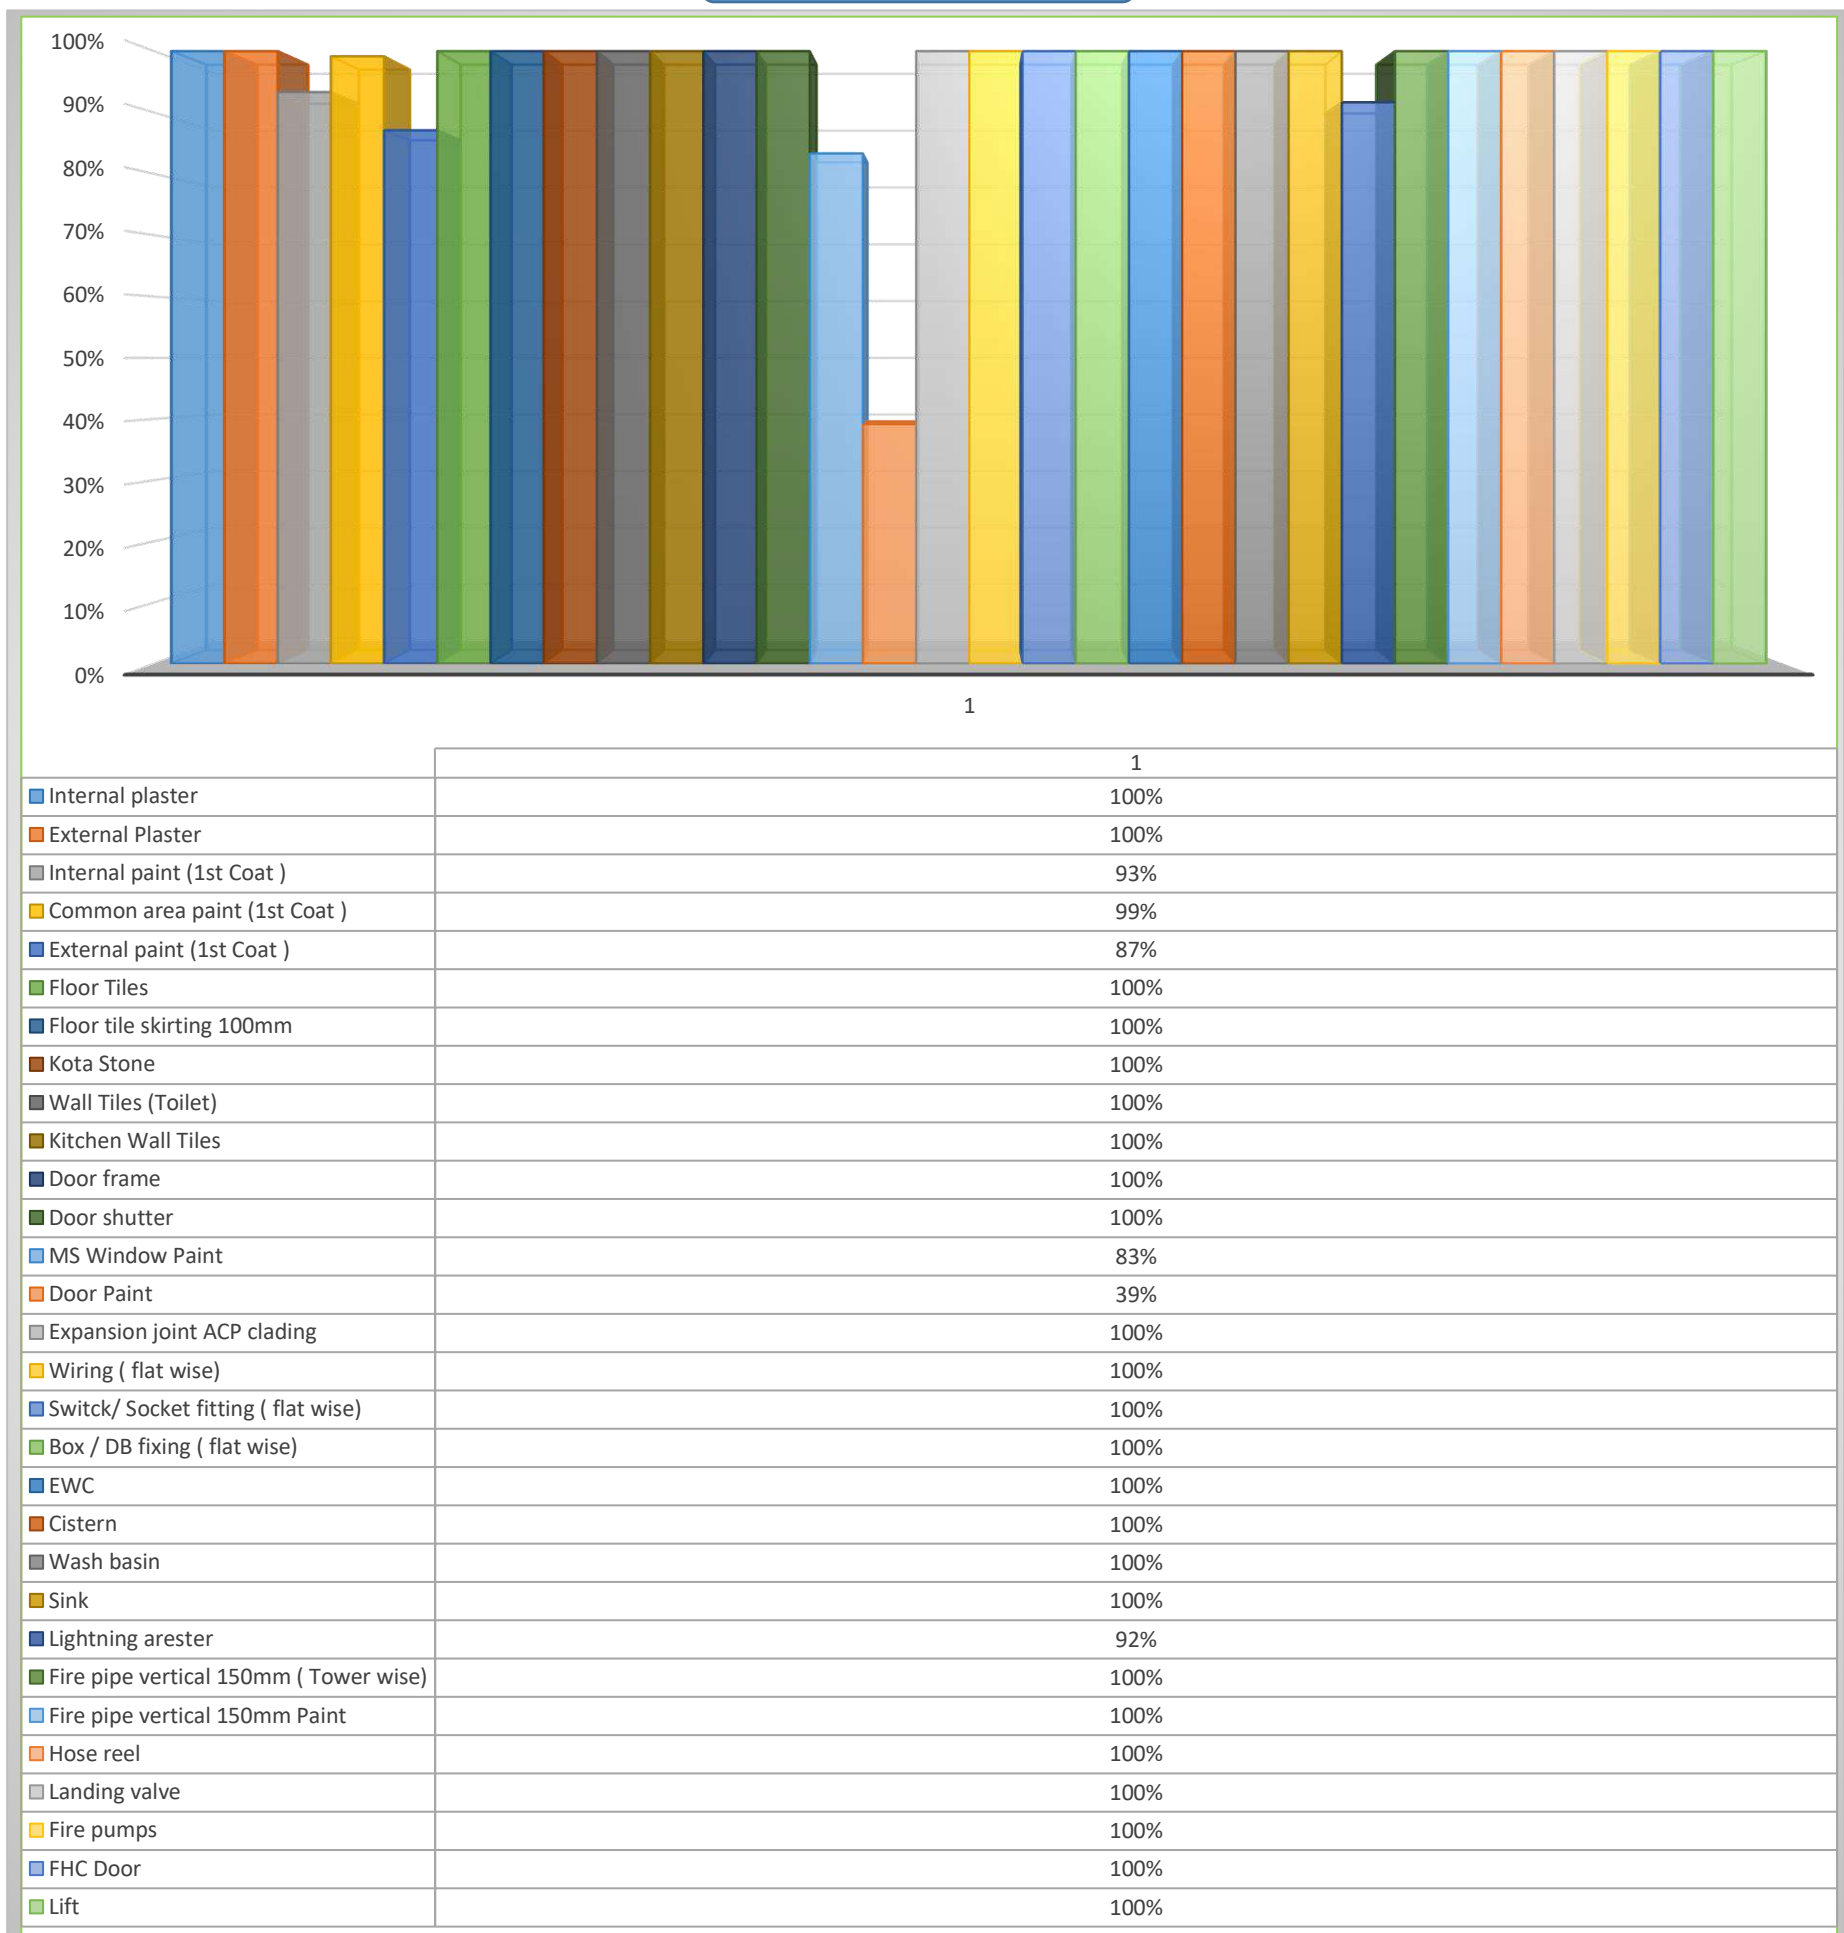

SUMMERIZED TOWER WISE WORK STATUS


Tower 18 & 19 Work Status

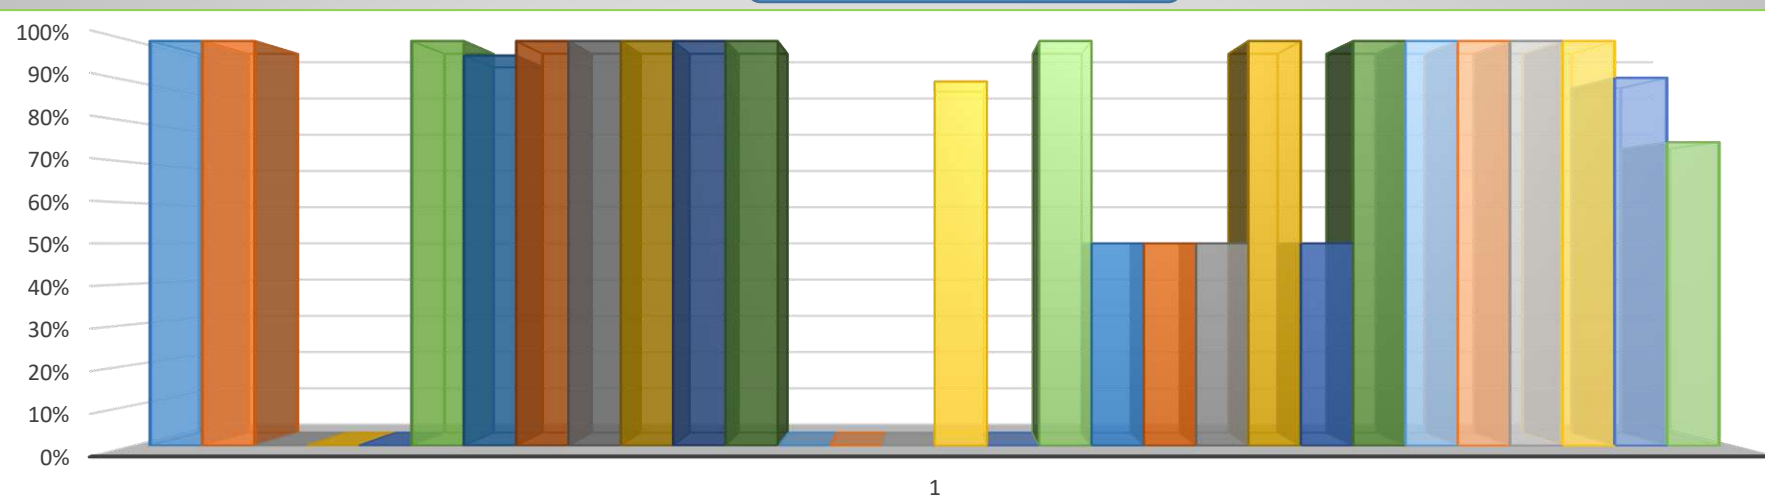

	1
Internal plaster	100%
External Plaster	100%
Internal paint (1st Coat)	0%
Common area paint (1st Coat)	0%
External paint (1st Coat)	0%
Floor Tiles	100%
Floor tile skirting 100mm	96%
Kota Stone	100%
Wall Tiles (Toilet)	100%
Kitchen Wall Tiles	100%
Door frame	100%
Door shutter	100%
MS Window Paint	0%
Door Paint	0%
Expansion joint ACP clading	-
Wiring (flat wise)	90%
Switch/ Socket fitting (flat wise)	0%
Box / DB fixing (flat wise)	100%
EWC	50%
Cistern	50%
Wash basin	50%
Sink	100%
Lightning arester	50%
Fire pipe vertical 150mm (Tower wise)	100%
Fire pipe vertical 150mm Paint	100%
Hose reel	100%
Landing valve	100%
Fire pumps	100%
FHC Door	91%
Lift	75%

SUMMERIZED TOWER WISE WORK STATUS

Common Infra Work status

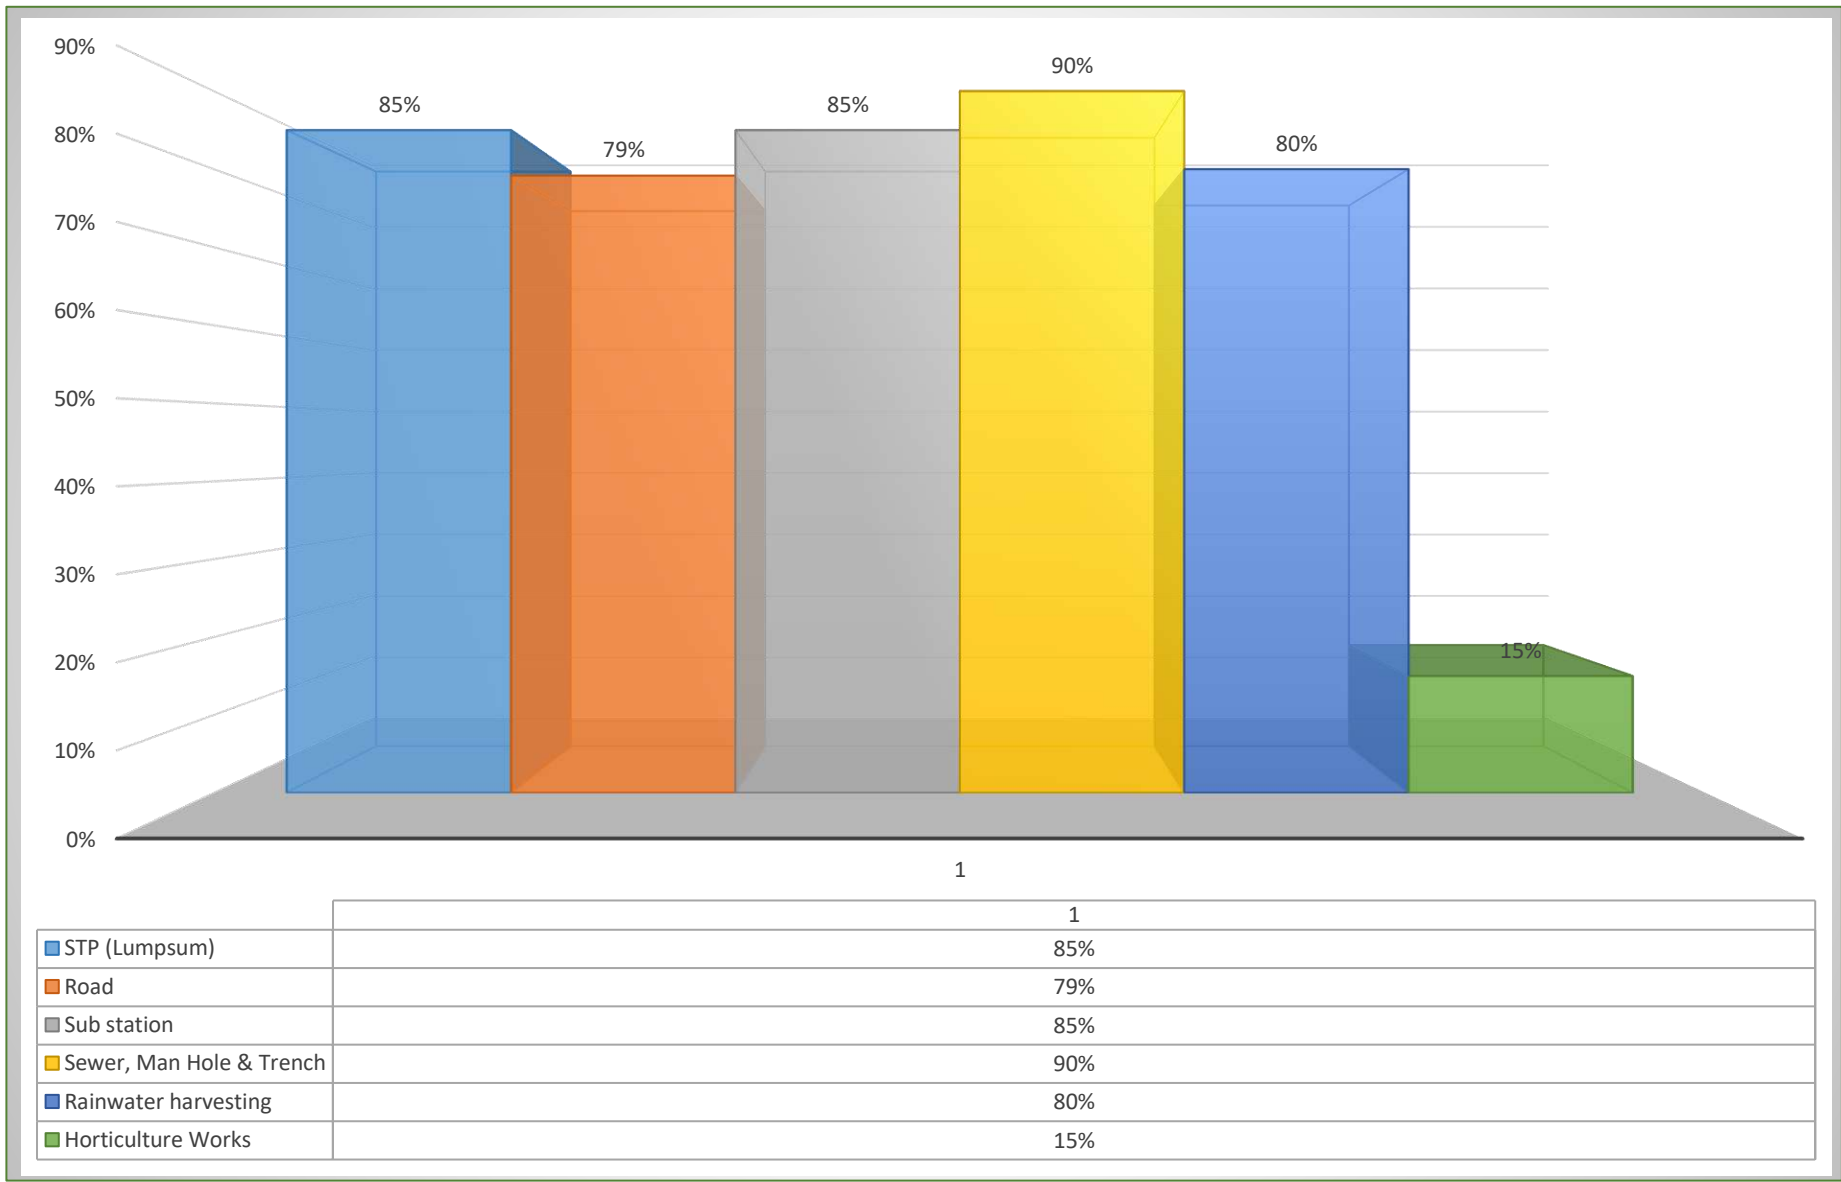

PROJECT: BREEZ GLOBAL HEIGHTS

SUMMERIZED TOWER WISE WORK STATUS

CBRE

Sl. No.	Work Description	Total Qty 1st to 5th	1st to 5th Work done qty	1st to 5th Percentage	Total Work qty 6th to 17th	Work done qty 6th to 17th	6th to 17th Percentage	Total Work qty 18th to 19th	18th to 19th work done qty	18th to 19th floor Percentage
1	Internal plaster	63,519.65	63,519.65	100%	1,52,447.16	1,52,447.16	100%	39,031.52	39,031.52	100%
2	External Plaster	18,733.93	18,367.93	98%	45,655.48	45,655.48	100%	12,679.88	12,679.88	100%
3	Internal paint (1st Coat)	54,354.20	19,870.91	37%	1,30,450.08	1,21,736.09	93%	32,399.72	-	0%
4	Common area paint (1st Coat)	9,165.45	-	0%	21,997.08	21,813.77	99%	6,631.80	-	0%
5	External paint (1st Coat)	18,733.93	-	0%	45,655.48	39,765.54	87%	12,679.88	-	0%
6	Floor Tiles	18,990.00	18,990.00	100%	45,576.00	45,576.00	100%	11,442.00	11,442.00	100%
7	Floor tile skirting 100mm	19,050.70	19,050.70	100%	45,721.68	45,721.68	100%	10,763.48	10,377.33	96%
8	Kota Stone	2,924.25	2,924.25	100%	7,018.20	7,018.20	100%	2,067.20	2,067.20	100%
9	Wall Tiles (Toilet)	7,992.00	7,992.00	100%	19,180.80	19,180.80	100%	4,562.56	4,562.56	100%
10	Kitchen Wall Tiles	1,174.50	1,174.50	100%	2,818.80	2,818.80	100%	671.11	671.11	100%
11	Door frame	2,000.00	2,000.00	100%	4,800.00	4,800.00	100%	1,200.00	1,200.00	100%
12	Door shutter	2,600.00	2,600.00	100%	6,240.00	6,240.00	100%	1,520.00	1,520.00	100%
13	MS Window Paint	1,400.00	-	0%	3,360.00	2,800.00	83%	840.00	-	0%
14	Door Paint	2,600.00	260.00	10%	6,240.00	2,444.00	39%	1,560.00	-	0%
15	Expansion joint ACP clading	4.00	4.00	100%	8.00	8.00	100%	N/A	N/A	N/A
16	Wiring (flat wise)	400.00	400.00	100%	960.00	960.00	100%	240.00	216.00	90%
17	Switch/ Socket fitting (flat wise)	400.00	240.00	60%	960.00	960.00	100%	240.00	-	0%
18	Box / DB fixing (flat wise)	400.00	400.00	100%	960.00	960.00	100%	240.00	240.00	100%
19	EWC	600.00	540.00	90%	1,440.00	1,440.00	100%	360.00	180.00	50%
20	Cistern	600.00	564.00	94%	1,440.00	1,440.00	100%	360.00	180.00	50%
21	Wash basin	600.00	564.00	94%	1,440.00	1,440.00	100%	360.00	180.00	50%
22	Sink	400.00	400.00	100%	960.00	960.00	100%	240.00	240.00	100%
23	Lightning arester	10.00	5.00	50%	24.00	22.00	92%	8.00	4.00	50%
24	Fire pipe vertical 150mm (Tower wise)	5.00	5.00	100%	12.00	12.00	100%	4.00	4.00	100%
25	Fire pipe vertical 150mm Paint	5.00	5.00	100%	12.00	12.00	100%	4.00	4.00	100%
26	Hose reel	60.00	60.00	100%	144.00	144.00	100%	48.00	48.00	100%
27	Landing valve	60.00	60.00	100%	144.00	144.00	100%	48.00	48.00	100%
28	Fire pumps	5.00	5.00	100%	12.00	12.00	100%	4.00	4.00	100%
29	FHC Door	55.00	55.00	100%	132.00	132.00	100%	44.00	40.00	91%
30	Lift	5.00	3.00	60%	12.00	12.00	100%	4.00	3.00	75%
	Common infra									
1	STP (Lumpsum)	1.00	0.85	85%						
2	Road	1.20	0.95	79%						
3	Sub station	1.00	0.85	85%						
4	Sewer, Man Hole & Trench	1.00	0.90	90%						
5	Rainwater harvesting	1.00	0.80	80%						
6	Solid waste management foundation	1.00	1.00	100%						
7	Horticulture Works	1.00	0.15	15%						

PROJECT: GLOBAL HEIGHTS																							
S.No.	ITEMS	Unit	Total Tower Wise Qty.																				TOTAL
			Tower 1	Tower 2	Tower 3	Tower 4	Tower 5	Tower 6	Tower 7	Tower 8	Tower 9	Tower 10	Tower 11	Tower 12	Tower 13	Tower 14	Tower 15	Tower 16	Tower 17	Tower 18	Tower 19	Tower 20	
	CIVIL																						
1	Plaster	Sq. Mtr.	17,630.78	17,413.89	17,379.67	17,379.67	17,596.56	17,596.56	17,596.56	17,596.56	17,596.56	17,596.56	17,346.96	17,596.56	17,596.56	17,379.67	17,379.67	17,379.67	17,596.56	27,351.70	27,305.08	1,151.20	3,53,466.94
a	Wall Plaster	Sq. Mtr.	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	11,714.59	11,714.59	369.64	1,56,167.62
b	Ceiling Plaster	Sq. Mtr.	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	4,485.27	4,485.27	102.06	61,508.07
c	Common Area	Sq. Mtr.	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	3,315.90	3,315.90	163.23	37,957.56
d	External Plaster	Sq. Mtr.	3,876.92	3,660.03	3,660.03	3,660.03	3,876.92	3,876.92	3,876.92	3,876.92	3,876.92	3,876.92	3,660.03	3,876.92	3,876.92	3,660.03	3,660.03	3,660.03	3,876.92	6,339.94	6,339.94	330.22	77,399.51
e	Stilt Plaster	Sq. Mtr.	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,113.44	1,496.00	1,496.00	185.87	22,106.35
2	Floor Tiles	Sq. Mtr.	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	5,721.00	5,721.00	136.37	76,144.37
3	Kota Stone	Sq. Mtr.	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	1,033.60	1,033.60		12,009.65
4	Floor tile Skirting 100mm	RM	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	5,381.74	5,381.74	121.82	75,657.68
5	Wall Tiles(Toilet)	Sq. Mtr.	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	2,281.28	2,281.28	49.93	31,785.29
6	Kitchen Counter	Sq. Mtr.	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	313.50	313.50	11.74	4,553.84
7	Kitchen Wall Tiles	Sq. Mtr.	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	335.56	335.56	12.14	4,676.56
8	Wooden Frame																						
a	Door 1(2400 x 1000 x 115)	Nos.	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	120.00	120.00	4.00	1,604.00
b	Door 2(2500 x 950 x 90)	Nos.	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	180.00	180.00	4.00	2,404.00
c	Door 3(2500 x 750 x 90)	Nos.	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	300.00	300.00	8.00	4,008.00
9	Wooden Frame(in Cu.mtrs)																						
a	Door 1(0.03988 Cu.mtrs))	Cu. Mtr.	-	3.19	3.19	3.19	3.19	3.19	3.19	3.19	3.19	3.19	3.19	3.19	3.19	3.19	3.19	3.19	3.19	4.79	4.79	0.16	60.78
b	Door 2(0.03105 Cu.mtrs)	Cu. Mtr.	2.48	2.48	2.48	2.48	2.48	2.48	2.48	2.48	2.48	2.48	2.48	2.48	2.48	2.48	2.48	2.48	2.48	5.59	5.59	0.12	53.53
c	Door 3(0.02925 Cu.mtrs))	Cu. Mtr.	3.51	3.51	3.51	3.51	3.51	3.51	3.51	3.51	3.51	3.51	3.51	3.51	3.51	3.51	3.51	3.51	3.51	8.78	8.78	0.23	77.45
10	Wooden Door																						
a	Door 1(2350 x 910 x 150)	Nos.	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	120.00	120.00	4.00	1,604.00
b	Door 2(2100 x 840 x 150	Nos.	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	180.00	180.00	4.00	2,404.00
c	Door 3(2100 x 660 x 125)	Nos.	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	300.00	300.00	8.00	4,008.00
d	Door4(2100 x 900 x 150)(MS Frame)	Nos.	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	160.00	160.00	4.00	2,364.00
11	MS Window	Nos.	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	120.00	120.00	4.00	1,604.00
12	MS Window	Nos.	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	140.00	140.00	4.00	1,644.00
13	MS Door+Window	Nos.	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	160.00	160.00	4.00	2,364.00
14	False Ceiling(Toilet)	Sq. Mtr.	268.80	268.80	268.80	268.80	268.80	268.80	268.80	268.80	268.80	268.80	268.80	268.80	268.80	268.80	268.80	268.80	268.80	471.00	471.00	14.40	5,526.00
15	Waterproofing	Sq. Mtr.	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	1,923.40	1,923.40	51.06	27,670.82
16	Paint+Putti Internal	Sq. Mtr.	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	16,227.06	1,923.40	514.85	2,01,808.09
	Paint+Putti External	Sq. Mtr.	5,710.01	5,493.12	5,493.12	5,493.12	5,710.01	5,710.01	5,710.01	5,710.01	5,710.01	5,710.01	5,493.12	5,710.01	5,710.01	5,493.12	5,493.12	5,493.12	5,710.01	9,655.84	9,655.84	990.66	1,15,854.28
17	Balcony Railings	RM	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	1,002.80	1,002.80	140.20	14,294.68
18	Staircase Railings	RM	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	171.12	171.12	25.98	3,399.66
	PLUMBING																						
1	WC(with Heath Faucet)	Nos.	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	180.00	180.00	4.00	2,404.00
2	Wash Basin with drain pipe	Nos.	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	180.00	180.00	4.00	2,404.00
3	Shower	Nos.	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	180.00	180.00	4.00	2,404.00
4	Tap(Toilet)	Nos.	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	720.00	720.00	16.00	9,616.00
5	Angle Valve	Nos.	520.00	520.00	520.00	520.00	520.00	520.00	520.00	520.00	520.00	520.00	520.00	520.00	520.00	520.00	520.00	520.00	520.00	760.00	760.00	16.00	10,376.00
6	Kitchen Sink with Drain Pipe	Nos.	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	120.00	120.00	4.00	1,604.00
7	Tap(Kitchen)	Nos.	160.00	160.00	160.00	160.00	160.00	160.00	160.00	160.00	160.00	160.00	160.00	160.00	160.00	160.00	160.00	160.00	160.00	200.00	200.00	8.00	3,128.00
8	Drain Cover(jali)	Nos.	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	480.00	680.00	680.00	20.00	9,540.00
		Nos.																					
	ELECTRICAL																						
1	Distribution Board	Nos.	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	120.00	120.00	4.00	1,604.00
2	Switch 6/10 Amps	Nos.	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
3	Socket 6/10 Amps	Nos.	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
4	Switch 25 Amps	Nos.	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-						

Work Status, Global Heights																								
S.No.	ITEMS	Unit	Work Done Qty.																				TOTAL	
			Tower 1	Tower 2	Tower 3	Tower 4	Tower 5	Tower 6	Tower 7	Tower 8	Tower 9	Tower 10	Tower 11	Tower 12	Tower 13	Tower 14	Tower 15	Tower 16	Tower 17	Tower 18	Tower 19	Tower 20		
	CIVIL																							
1	Plaster																							
a	Wall plaster	Sq. Mtr.	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	7,786.40	11,714.59	11,714.59	369.64	1,56,167.62	
b	Ceiling plaster	Sq. Mtr.	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	3,084.44	4,485.27	4,485.27	102.06	61,508.07	
c	Common area plaster	Sq. Mtr.	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	3,315.90	3,315.90	163.23	37,957.56	
d	External plaster	Sq. Mtr.	3,876.92	3,477.03	3,477.03	3,660.03	3,876.92	3,876.92	3,876.92	3,876.92	3,876.92	3,876.92	3,876.92	3,660.03	3,876.92	3,876.92	3,660.03	3,660.03	3,660.03	3,876.92	6,339.94	6,339.94	330.22	77,033.51
2	Floor Tiles	Sq. Mtr.	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	3,798.00	5,721.00	5,721.00	136.37	76,144.37	
4	Floor tile Skirting 100mm	RM	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	3,810.14	4,995.59	5,381.74	121.82	75,271.53	
3	Kota Stone	Sq. Mtr.	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	584.85	1,033.60	1,033.60	88.00	12,097.65	
5	Wall Tiles(Toilet)	Sq. Mtr.	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	1,598.40	2,281.28	2,281.28	49.93	31,785.29	
6	Kitchen Counter	Sq. Mtr.	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	230.30	313.50	313.50	11.74	4,553.84	
7	Wall Tiles (Kitchen)	Sq. Mtr.	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	234.90	335.56	335.56	12.14	4,676.56	
																							-	
8	Wooden Frame																						-	
a	Door 1(2400 x 1000 x 115)	Nos.	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	120.00	120.00	4.00	1,604.00	
b	Door 2(2500 x 950 x 90)	Nos.	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	180.00	180.00	4.00	2,404.00	
c	Door 3(2500 x 750 x 90)	Nos.	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	300.00	300.00	8.00	4,008.00	
																							-	
9	Wooden Door shutter																						-	
a	Door 1(2350 x 910 x 150)	Nos.	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	120.00	120.00	4.00	1,604.00	
b	Door 2(2100 x 840 x 150	Nos.	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	180.00	180.00	4.00	2,404.00	
c	Door 3(2100 x 660 x 125)	Nos.	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	200.00	300.00	300.00	4.00	4,004.00	
d	Door4(2100 x 900 x 150)(MS Frame)	Nos.	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	160.00	160.00	4.00	2,364.00	
10	MS Window	Nos.	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	120.00	120.00	4.00	1,604.00	
11	MS Window	Nos.	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	80.00	140.00	140.00	4.00	1,644.00	
12	MS Door+Window	Nos.	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	120.00	160.00	160.00	4.00	2,364.00	
13	False Ceiling(Toilet)	Sqmtrs.	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
14	Waterproofing	Sq. Mtr.	1,398.41	1,398.41	1,398.41	1,398.41	1,398.41	724.24	724.24	724.24	724.24	724.24	724.24	724.24	724.24	724.24	724.24	724.24	724.24	1,923.40	1,923.40	51.06	19,580.78	
15	Putti Internal Flats	Sq. Mtr.	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	10,773.11	8,113.53	10,517.55	514.85	2,02,288.71	
16	Putti Lobby	Sq. Mtr.	1,558.13	1,283.16	1,283.16	1,466.47	916.55	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,657.95	2,818.52	660.44	33,641.45	
17	Primer External	Sq. Mtr.	-	-	-	-	-	3,876.92	3,876.92	3,876.92	3,876.92	3,876.92	3,876.92	3,660.03	3,876.92	3,876.92	3,660.03	3,660.03	3,660.03	3,876.92	6,339.94	6,339.94	330.22	58,665.58
18	Paint Internal Flats (1st coat OBD)	Sq. Mtr.	9,417.35	10,453.56	-	-	-	8,618.48	9,695.79	9,695.79	8,618.48	10,773.11	10,773.11	10,773.11	9,695.79	10,773.11	10,773.11	10,773.11	10,773.11	-	-	514.85	1,42,121.85	
19	Paint Lobby	Sq. Mtr.	-	-	-	-	-	1,833.09	1,833.09	1,833.09	1,649.78	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	1,833.09	-	-	-	21,813.77	
20	Paint External	Sq. Mtr.	-	-	-	-	-	3,101.54	3,101.54	3,876.92	3,489.23	3,294.03	3,489.23	2,713.84	2,928.02	3,294.03	3,111.03	3,489.23	-	-	330.22	40,095.76		
21	Balcony Railings	Sq. Mtr.	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	714.64	1,002.80	1,002.80	28.04	14,182.52	
22	Staircase railing	Sq. Mtr.	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	178.32	209.76	273.12	25.98	3,540.30	

[illegible]



RESPECT/INTEGRITY/SERVICE/EXCELLENCE

RESPECT :: INTEGRITY :: SERVICE :: EXCELLENCE

Our corporate values are the foundation upon which our company is built. These values are timeless and transcend all markets, service lines, languages and business cultures.



Gracias. Thank You. 謝謝. Salamat. Obrigado. شكرا
Спасибо. 감사합니다. បាទបាទ. Danke. ありがとう. Merci.

Strategic consulting | Valuation & Advisory | Services | Office Services | Retail Services | Residential Services | Land & industrial | Industrial and Logistics Services | Project Marketing | Project Management | Asset Services | Facilities Management | Property Management | Global Corporate Services | Capital Markets

PROJECT MANAGEMENT

PROJECT MANAGEMENT
PROJECT MONITORING
TECHNICAL DUE DILIGENCE
OHSE & QUALITY AUDITS
COST CONSULTANCY
INDUSTRIAL SERVICES
DESIGN SERVICES

This document provided by CBRE is privileged and confidential in nature. This document is for the sole usage of the Recipient, its authorized affiliates, designates, and assignees and no other party shall have any right to use this document without prior written approval of CBRE. Further, the document shall neither be disseminated or circulated without prior written approval from CBRE
